



# EPL 21807 Monitoring Report December 2025

SSMWSASSM-PLD-1NL-NL000-EV-RPT-000044

Parklife Metro D&C

## Approval Record

Revision	Author	Date	Issue	Reviewed by	Approved by
00	[REDACTED]	07/01/2026	Initial Draft	[REDACTED]	[REDACTED]
<b>Signature</b>		[REDACTED]			

---

## Contents

<b>1</b>	<b>Introduction</b>	<b>5</b>
1.1	Background	5
1.1.1	Stations, Systems, Trains, Operations and Maintenance works	5
1.2	Scope of this report	7
<b>2</b>	<b>Reporting requirements</b>	<b>8</b>
<b>3</b>	<b>Monitoring</b>	<b>18</b>
3.1	Weather Monitoring	18
3.2	Noise and Vibration Monitoring	18
3.3	Water Monitoring	20
3.3.1	Surface water monitoring	20
3.3.2	Discharge to water	20
<b>Appendix A</b>	<b>Weather Observations</b>	<b>25</b>
<b>Appendix B</b>	<b>Noise Monitoring</b>	<b>26</b>
<b>Appendix C</b>	<b>Discharge to water</b>	<b>28</b>
<b>Appendix D</b>	<b>Surface water monitoring</b>	<b>29</b>
<b>Appendix E</b>	<b>Premise Maps – December</b>	<b>30</b>

---

## Table of Figures

FIGURE 1 OVERVIEW OF SMWSA PROJECT .....	6
--	---

## Table of Tables

TABLE 1 LICENCE DETAILS .....	7
TABLE 2 EPL 21807 MONITORING REQUIREMENTS .....	9
TABLE 3 WEATHER SUMMARY AND TRIGGER WEATHER EVENTS FOR REPORTING PERIOD .....	18
TABLE 4 SUMMARY OF NOISE MONITORING FOR REPORTING PERIOD .....	19
TABLE 5 MONITORING/DISCHARGE POINTS AND AREAS .....	21
TABLE 6 MONTHLY WEATHER OBSERVATION TABLE .....	25
TABLE 7 DETAILED NOISE MONITORING DATA.....	26
TABLE 8 WATER DISCHARGE TABLE .....	28

# 1 Introduction

## 1.1 Background

Sydney Metro is Australia's biggest public transport program comprising four main packages of work including Metro North-West Line, Sydney Metro City and Southwest, Sydney Metro West, and Sydney Metro Western Sydney Airport (SMWSA, the Project). The SMWSA will become the transport spine for Greater Western Sydney, connecting communities and travellers with the new Western Sydney International (Nancy-Bird Walton) Airport (referred to as Western Sydney International) and the growing region.

The Project involves the construction and operation of a new metro railway line around 23km in length that extends from the existing Sydney Trains suburban T1 Western Line at St Marys in the north to the new Bradfield Station in the south at Bringelly. The alignment includes a combination of tunnel, surface, bridges and viaduct sections, and comprises of six new metro stations between St Marys and the Bradfield Core precinct, as well as a stabling and maintenance facility and operational control centre to support the operation of the new metro railway line (see Figure 1).

### 1.1.1 Stations, Systems, Trains, Operations and Maintenance works

Parklife Metro D&C has been engaged to deliver the Stations, Systems, Trains, Operations and Maintenance (SSTOM) works. The scope of the Stations, Systems, Trains, Operations and Maintenance (SSTOM) package comprises:

- construction of the six new stations
- installation of tracks, signalling, mechanical and electrical systems
- supplying new driverless trains
- construction of stabling and maintenance facility at Orchard Hills
- operation and maintenance of the line and its assets, and
- handback of operations and maintenance at the end of term.



FIGURE 1 OVERVIEW OF SMWSA PROJECT

## 1.2 Scope of this report

Parklife Metro D&C have been issued an Environment Protection Licence (EPL No. 21807) from the NSW Environment Protection Authority (EPA) for the SMWSA SSTOM Works. The EPL applies to the works approved under the Infrastructure Approval SSI-10051 associated with the delivery of the off-airport portion of the SMWSA SSTOM Works, as detailed in Table 1. This EPL Monitoring Report provides the results of all pollution monitoring required to be measured or monitored by the licensee of EPL 21807 within the reporting period as required by Section 66 of the *Protection of the Environment Operations Act 1997* (POEO Act) and with reference to EPA Publication *Requirements for publishing pollution monitoring data* (Environment Protection Authority, 2013).

TABLE 1 LICENCE DETAILS

<b>Licence Details</b>	
<b>Number</b>	21807
<b>Copy of Licence</b>	<a href="#">Environment &amp; Heritage   POEO Licences, Application and Notice Detail (nsw.gov.au)</a>
<b>Anniversary Date</b>	20-July
<b>Licensee</b>	WEBUILD S.P.A
<b>Premises</b>	SYDNEY METRO WESTERN SYDNEY AIRPORT SSTOM PACKAGE FOOTPRINT  SYDNEY METRO WESTERN SYDNEY AIRPORT-STATIONS, SYSTEMS, TRAINS, OPERATION & MAINTENANCE PACKAGE
<b>Scheduled Activity</b>	Railway activities – railway infrastructure construction

## 2 Reporting requirements

Under the POEO Act, holders of environment protection licences (licensees) must publish or make pollution monitoring data available to members of the public.

The POEO Act Section 66 requires:

*"Conditions requiring monitoring, certification or provision of information, and related offences*

*(1) Monitoring The conditions of a licence may require—*

- (a) monitoring by the holder of the licence of the activity or work authorised, required or controlled by the licence, including with respect to—*
  - (i) the operation or maintenance of premises or plant, and*
  - (ii) discharges from premises, and*
  - (iii) relevant ambient conditions prevailing on or outside premises, and*
  - (iv) anything required by the conditions of the licence, and*
- (b) the provision and maintenance of appropriate measuring and recording devices for the purposes of that monitoring, and*
- (c) the analysis, reporting and retention of monitoring data.*

*(2) False or misleading information A holder of a licence who supplies information, or on whose behalf information is supplied, to the appropriate regulatory authority under the conditions of the licence is guilty of an offence if the information is false or misleading in a material respect."*

The primary objective of the EPL Monitoring Report is that members of the public have access to the results of all pollution monitoring (which a licence specifies must be carried out) in a way that is meaningful to them.

The monitoring data that must be published and/or made available on request is any data that is obtained as a result of a monitoring condition on a licence that relates to air, water (surface or groundwater), noise and/or land pollution. The data to be published or provided is limited to data that relates to pollutants generated, discharged or emitted from the licensed premises.

The data is provided in tabular format that is easy for the general public to understand. Tables definitively display raw data values, while graphs and charts are useful for overviews and visualisation of long-term trends. Raw data will be provided upon request.

This EPL Monitoring Report will provide explanations as to why data may appear to be missing, which may be due to there being no discharge or the level of pollutant being below the detection level of the measurement instrument.

It's possible from time to time that incorrect data may get published in good faith. As soon as practicable after the licensee becomes aware that the published pollution monitoring data is incorrect or misleading, licensees must then publish a correction log to correct this data that is incorrect or misleading.

Table 2 provides a summary of the monitoring requirements of EPL 21807.

**TABLE 2 EPL 21807 MONITORING REQUIREMENTS**

EPL Condition	Requirement	Report Reference
<b>Weather</b>		
M5.1	<p>The licensee must monitor and record temperature, wind direction, wind velocity and rainfall at either the project weather station, or through analysis of equivalent weather information obtained from the Australian Bureau of Meteorology. Monitoring must:</p> <ul style="list-style-type: none"> <li>a) be representative of the premises;</li> <li>b) commence prior to any works that may cause sediment to leave the premises; and</li> <li>c) continue to be operated until soil disturbance activities cease at the premises and the site has been stabilised.</li> </ul>	Section 3.1 Appendix A
<b>Noise</b>		
L5.9	<p>Works outside of standard construction hours – Regulatory Requirements</p> <p>In undertaking any works and activities outside of standard construction hours under condition L5.8, the licensee must comply with the following:</p> <ul style="list-style-type: none"> <li>a) Prepare a construction noise and vibration impact assessment in accordance with the Interim Construction Noise Guideline (DEC, 2009) that is to include: <ul style="list-style-type: none"> <li>i. a description of the proposed works and activities outside of standard construction hours;</li> <li>ii. predictions of LAeq (15 minute) dB noise levels at noise sensitive receivers from these works and activities, where noise levels are predicted to be greater than those permitted under condition L5.3; and</li> <li>iii. a monitoring plan to validate the noise predictions, based on monitoring at the boundary of representative sensitive receivers during noise generating activities that are representative of the works and activities, including during the period/s predicted to have the highest noise level impacts.</li> </ul> </li> <li>b) Undertake noise monitoring in accordance with the monitoring plan required by condition L5.9(a)(iii).</li> </ul>	Section 3.2 Appendix B

L5.10	<p>St Marys Station, Orchard Hills Station and Bradfield Station - Out of Hours Concrete Works</p> <p>Concrete works associated with station box construction at St Marys Station, Orchard Hills Station and Bradfield Station, including concrete pouring, finishing and cleaning, are permitted to be undertaken outside of standard construction hours specified in L5.1 provided that:</p> <ul style="list-style-type: none"> <li>a) Works are required to achieve compliance with overarching project technical requirements,</li> <li>b) Works had already begun within a reasonable time prior to end of standard construction hours,</li> <li>c) Out of Hours (OOH) works are undertaken from 5am to 7am and 6pm to 12am (midnight), Monday to Friday and 6am to 8am and 1pm to 6pm on Saturday,</li> <li>d) Station box base slab and wall concreting activities and supporting formwork and reinforcement activities are permitted to occur up to 12am (midnight) Monday to Friday a total of 12 times per month until all base slabs and wall pours are completed,</li> <li>e) Station box base slab and wall concreting activities and supporting formwork and reinforcement activities (e.g. using concrete pump, vibrators, concrete trucks, etc) must be completed before 12am (midnight) on Monday to Friday,</li> <li>f) All other concreting activities (e.g. using concrete pump, vibrators, concrete trucks, etc) must be completed before 10pm on Monday to Friday,</li> <li>g) Concrete finishing works (e.g. power floats, hand tools) must be completed before 12am (midnight) on Monday to Friday,</li> <li>h) The licensee is required to undertake noise monitoring in accordance with condition L5.9(b),</li> <li>i) The licensee is required to undertake noise monitoring on a monthly basis at each Station and additionally monitor the first three instances of OOH concrete works at each Station: <ul style="list-style-type: none"> <li>1. commencing prior to 7am, and</li> <li>2. extending past 10pm</li> </ul> </li> <li>j) The licensee is required to provide the EPA with a Noise Monitoring Report within 30 days of the end of each month,</li> <li>k) Works are permitted to occur until 31 May 2026.</li> </ul>	Section 3.2 Appendix B
L5.11	<p>St Marys, Orchard Hills and Bradfield Station sites - Out of Hours Precast Concrete Beam Installation</p> <p>Precast beam installation for station box construction at St Marys, Orchard Hills and Bradfield Station sites is permitted to be undertaken outside of standard construction hours specified in L5.1, provided that:</p> <ul style="list-style-type: none"> <li>a) Works are required to achieve compliance with project requirements for unloading oversize/overmass precast beam deliveries and site safety requirements,</li> <li>b) Works and activities are undertaken from 12am (midnight) to 7am, Monday to Friday nights,</li> <li>c) The licensee is required to undertake noise monitoring in accordance with condition L5.9(b),</li> <li>d) The licensee is required to undertake noise monitoring at each Station on a monthly basis, and additionally monitor: <ul style="list-style-type: none"> <li>1. the first two instances of OOH concrete beam installation at each Station, and</li> <li>2. the first two instances of OOH concrete beam installation at each Station that occurs concurrently with activities permitted under Condition L5.10.</li> </ul> </li> <li>e) The licensee is required to provide the EPA with a Noise Monitoring Report within 30 days of the end of each month,</li> <li>f) Works are permitted to occur until 31 May 2026.</li> </ul>	Section 3.2 Appendix B

L5.12	<p>Stabling and Maintenance Facility - Out of Hours Concrete Works Concrete works associated with Maintenance &amp; Administration and Operational Control Centre buildings at the Stabling and Maintenance Facility, including concrete pouring, finishing, and cleaning, are permitted to be undertaken outside of standard construction hours specified in L5.1 provided that:</p> <ul style="list-style-type: none"> <li>a) Works are required to achieve compliance with overarching project technical requirements,</li> <li>b) Works had already begun within a reasonable time prior to end of standard construction hours,</li> <li>c) Out of Hours works (OOH) are undertaken from 5am to 7am and 6pm to 12am (midnight), Monday to Friday, and 6am to 8am, and 1pm - 6pm on Saturday,</li> <li>d) Base slab concreting activities and supporting formwork and reinforcement activities must be completed before 12am (midnight) Monday to Friday,</li> <li>e) Base slab concreting activities and supporting formwork and reinforcement activities are permitted to occur up to 12am (midnight) Monday to Friday a total of 12 times per month until base slabs are completed,</li> <li>f) All other concreting activities (e.g. using concrete pump, vibrators, concrete trucks, etc) must be completed before 10pm on Monday to Friday,</li> <li>g) Concrete finishing works (e.g. power floats, hand tools) must be completed before 12am (midnight) on Monday to Friday,</li> <li>h) The licensee is required to undertake noise monitoring in accordance with L5.9(b),</li> <li>i) The licensee is required to undertake noise monitoring on a monthly basis and additionally during the first three instances of OOH concrete works: <ul style="list-style-type: none"> <li>1. commencing prior to 7am, and</li> <li>2. extending past 10pm.</li> </ul> </li> <li>j) The licensee is required to provide the EPA with a Noise Monitoring Report within 30 days of the end of each month,</li> <li>k) Works are permitted to occur until 31 March 2026.</li> </ul>	Section 3.2 Appendix B
L5.13	<p>Orchard Hills Station site - Out of Hours Concrete Batch Plant Operation The concrete batch plant located at the Orchard Hills site is permitted to operate outside of standard construction hours specified in L5.1 provided that:</p> <ul style="list-style-type: none"> <li>a) Operation of the plant is required to achieve compliance with overarching project technical requirements of large concrete pours permitted by condition L5.10 and L5.12</li> <li>b) Concrete works had already begun within a reasonable time prior to end of standard construction hours,</li> <li>c) Out of Hours (OOH) works are undertaken from 5am to 7am and 6pm to 10pm Monday to Friday, and 6am to 8am and 1pm to 6pm on Saturday,</li> <li>d) The licensee is required to undertake noise monitoring in accordance with condition L5.9(b),</li> <li>e) The licensee is required to undertake noise monitoring on a monthly basis and additionally monitor the first three instances of OOH operation of the concrete batch plant: <ul style="list-style-type: none"> <li>1. commencing prior to 7am, and</li> <li>2. extending past 8pm</li> </ul> </li> <li>f) The licensee is required to provide the EPA with a Noise Monitoring Report within 30 days of the end of each month,</li> <li>g) Works are permitted to occur until 31 May 2026.</li> </ul>	Section 3.2 Appendix B

L5.14	<p>Works outside standard construction hours - 24-hour works</p> <p>a) The following works are permitted to be undertaken 24 hours a day, 7 days per week for activities at the St Marys Station Site, Claremont Meadows services shaft site, Orchard Hills Station site, Bringelly services shaft site, and Bradfield Station site:</p> <ul style="list-style-type: none"> <li>i. Tunnel and underground station box fit out works and ancillary surface support works</li> <li>ii. Haulage and delivery of materials to the Claremont Meadows services shaft site and Bringelly services shaft site.</li> </ul> <p>b) The licensee is required to undertake attended noise monitoring:</p> <ol style="list-style-type: none"> <li>1. on the first two occasions of 24-hour works at each site: <ul style="list-style-type: none"> <li>i. St Marys Station site,</li> <li>ii. Claremont Meadows services shaft site,</li> <li>iii. Orchard Hills Station site,</li> <li>iv. Bringelly services shaft site,</li> <li>v. Bradfield Station site, and</li> </ul> </li> <li>2. noise monitoring must occur in the night time period.</li> <li>3. the licensee is required to provide the EPA with a Noise Monitoring Report within 30 days of the end of the month in which noise monitoring was undertaken.</li> </ol>	
L5.15	<p>Aluminothermic Welding and Rail Adjustments associated with rail installation at the Stabling and Maintenance facility, including rail cutting, riser removal and shearing and grinding of weld, are permitted to be undertaken outside of standard construction hours specified in L5.1 provided that:</p> <p>a) Works are required to achieve compliance with overarching project technical requirements,</p> <p>b) Works are commenced in the evening work period as soon as technically feasible within the required temperature constraints,</p> <p>c) Out of Hours (OOH) works are undertaken from 6pm to 3am Monday to Friday (completed by 3am Saturday morning),</p> <p>d) The licensee is required to undertake noise monitoring:</p> <ul style="list-style-type: none"> <li>i) on a monthly basis and during the first three aluminothermic welding and rail adjustment occasions; and</li> <li>ii) provide the EPA with a Noise Monitoring Report within 30 days of the end of the month in which monitoring occurred,</li> </ul> <p>e) Works are permitted to occur until 31 March 2026.</p>	Not triggered
M4.4	<p>The licensee must undertake noise and vibration monitoring as directed by an authorised officer of the EPA. Where the monitoring is requested to take place on private land (for example a residential property) the licensee must request permission to access the premises in advance and keep a record of permission requests and responses. If a licensee is unable to obtain permission, the licensee must undertake the monitoring at an indicative location where possible and they must provide the response (including any nil response) to the EPA.</p>	Not triggered

### Community Agreements

The licensee may work outside standard construction hours (as defined in L5.1) in circumstances other than those permitted under conditions L5.3, L5.4, or any other condition of the licence, subject to the condition outlined Section E1.

E1.4	<p>A noise validation monitoring plan must be submitted to the EPA for approval as part of the community agreement documentation prior to any OOHW occurring.</p>	Section 3.2 Appendix B
------	---	---------------------------

E1.5	<p>Validation monitoring must be undertaken for any OOHW that are the approved under condition E1.1 and must:</p> <ul style="list-style-type: none"> <li>a) be undertaken in accordance with the monitoring plan prepared under condition E1.4;</li> <li>b) be performed by a Competent Person;</li> <li>c) be performed on at least the first 2 occasions (day, evening, nights) where OOHW will be undertaken and are likely to impact Noise Sensitive Receivers;</li> <li>d) be performed on any other occasion (day, evening, night) where the nature of the works is likely to cause greater noise impacts than the first 2 occasions;</li> <li>e) be representative of the impacts in terms of monitoring locations, time and duration of measurements; and</li> <li>f) be recorded and provided to an EPA officer upon request.</li> </ul>	Section 3.2 Appendix B
------	---	---------------------------

**Water**

P1.1	The following points referred to in the table are identified in this licence for the purposes of the monitoring and/or the setting of limits for discharges of pollutants to water from the point.				<b>Section 3.3.2</b> <b>Table 5</b>
	<b>EPA Identification no</b>	<b>Type of Monitoring Point</b>	<b>Type of Discharge Point</b>	<b>Location Description</b>	
	1	Discharge and Monitoring	Discharge and Monitoring	The outlet of the sediment basin on the Bradfield site discharging to Thompson Creek referred to in Condition P1.2	
	2	Discharge and Monitoring	Discharge and Monitoring	The outlet of the water treatment plant on the St Marys site discharging to South Creek	
	3	Discharge and Monitoring	Discharge and Monitoring	The outlet of the sediment basin on the Orchard Hills site discharging to an Unnamed Creek (tributary of South Creek) referred to in Condition P1.2	
	4	Discharge and Monitoring	Discharge and Monitoring	The outlet of the water treatment plant on the Bradfield site discharging to Thompson Creek	
	5	Discharge and Monitoring	Discharge and Monitoring	The outlet of the sediment basin at the Stabling and Maintenance Facility site discharging to Blaxland Creek referred to in Condition P1.2	
	6	Discharge and Monitoring	Discharge and Monitoring	The outlet of the sediment basin discharging to Cosgroves Creek referred to in Condition P1.2	
	7	Discharge and Monitoring	Discharge and Monitoring	The outlet of the sediment basin on Orchard Hills site discharging to South Creek referred to in Condition P1.2	
	8	Discharge and Monitoring	Discharge and Monitoring	The outlet of the sediment basin near Elizabeth Drive discharging to Badgerys Creek referred to in Condition P1.2	
	9	Discharge and Monitoring	Discharge and Monitoring	The outlet of the sediment basin at the Claremont Meadows site discharging to local stormwater referred to in Condition P1.2.	
	10	Discharge and Monitoring	Discharge and Monitoring	The outlet of the sediment basin at the Claremont Meadows site discharging to local stormwater referred to in Condition P1.2.	
	11	Discharge and Monitoring	Discharge and Monitoring	The outlet of the sediment basin discharging to an unnamed tributary of Blaxland Creek referred to in Condition P1.2.	
	12	Discharge and Monitoring	Discharge and Monitoring	The outlet of the sediment basin on the Stabling and Maintenance Facility site discharging to Blaxland Creek referred to in Condition P1.2	
	13	Discharge and Monitoring	Discharge and Monitoring	The outlet of the sediment basin located south of Patons Lane discharging to an unnamed tributary of South Creek referred to in Condition P1.2	
	14	Discharge and Monitoring	Discharge and Monitoring	The outlet of the sediment basin at the Bringelly site discharging to Badgerys Creek referred to in Condition P1.2.	
	15	Discharge and Monitoring	Discharge and Monitoring	The outlet of the sediment basin near Luddenham Station	

			discharging to an unnamed tributary of South Creek referred to in Condition P1.2	
16	Discharge and Monitoring	Discharge and Monitoring	The outlet of the sediment basin on the Linewide North site discharging to Blaxland Creek referred to in Condition P1.2	
17	Discharge and Monitoring	Discharge and Monitoring	The outlet of the sediment basin on the Bradfield site discharging to Thompson Creek referred to in Condition P1.2	

M2.2	Water and/or Land Monitoring Requirements POINT 1, 3, 5, 6, 7, 8, 9, 10, 11, 12, 13, 14, 15, 16, 17				Section 3.3.2 Appendix C	
	<b>Pollutant</b>	<b>Unit of measure</b>	<b>Frequency</b>	<b>Sampling Method</b>		
	Oil and Grease	Visible	Special Frequency 1	Visual inspection		
	pH	pH	Special Frequency 1	Probe		
	Turbidity	nephelometric turbidity units	Special Frequency 1	Probe		
	POINT 2					
	<b>Pollutant</b>	<b>Units of measure</b>	<b>Frequency</b>	<b>Sampling Method</b>		
	Aluminium	milligrams per litre	Daily during any Grab sample discharge	Grab sample		
	Ammonia	milligrams per litre	Daily during any Grab sample discharge	Grab sample		
	Chromium (VI) Compounds	milligrams per litre	Daily during any discharge	Grab sample		
	Copper	milligrams per litre	Daily during any discharge	Grab sample		
	Electrical conductivity	microsiemens per centimetre	Daily during any discharge	Grab sample		
	Nitrogen (total)	milligrams per litre	Daily during any discharge	Grab sample discharge		
	Oil and Grease	Visible	Daily during any discharge	Visual Inspection		
	pH	pH	Daily during any discharge	Probe		
	Phosphorus (total)	milligrams per litre	Daily during any discharge	Grab sample		
	TSS	milligrams per litre	Daily during any discharge	Grab sample		
	Zinc	milligrams per litre	Daily during any discharge	Grab sample		
	POINT 4					
	<b>Pollutant</b>	<b>Units of measure</b>	<b>Frequency</b>	<b>Sampling Method</b>		
	Aluminium	milligrams per litre	Monthly during discharge	Grab sample		
	Ammonia	milligrams per litre	Monthly during discharge	Grab sample		
	Chromium (VI) Compounds	milligrams per litre	Monthly during discharge	Grab sample		
	Copper	milligrams per litre	Monthly during discharge	Grab sample		
	Electrical conductivity	microsiemens per centimetre	Monthly during discharge	Grab sample		
	Nitrogen (total)	milligrams per litre	Monthly during discharge	Grab sample		
	Oil and Grease	Visible	Monthly during discharge	Visual Inspection		
	pH	pH	Monthly during discharge	Probe		
	Phosphorus (total)	milligrams per litre	Monthly during discharge	Grab sample		
	TSS	milligrams per litre	Monthly during discharge	Grab sample		
	Zinc	milligrams per litre	Monthly during discharge	Grab sample		
M2.3	For the purposes of Condition M2.2 and the Table thereto, 'Special Frequency 1' means: a) less than 24 hours prior to a controlled discharge and daily for any continued controlled discharge, when it is safe to do so; and b) when rainfall causes a discharge from a sediment basin which has not been emptied within the design management period following cessation of a rainfall event, when it is safe to do so.				Section 3.3.2	

E2.1	<p>The licensee must undertake surface water monitoring of receiving waterways at locations upstream, downstream and adjacent to discharge points 2 and 4 identified in Condition P1.1 at fortnightly intervals and at least once during each discharge event. This monitoring must be undertaken for a minimum of 3 months:</p> <ul style="list-style-type: none"> <li>a) from the date that point 2 was added to the licence; and</li> <li>b) from the date that discharge from point 4 commences.</li> </ul> <p>Surface water monitoring results must include:</p> <ul style="list-style-type: none"> <li>a) quality and quantity of all parameters that are identified in the table in M2.2 for discharge points 2 and 4; and</li> <li>b) results must be submitted to the EPA no more than 2 weeks after each monitoring event has occurred for a minimum of 3 months:</li> </ul> <ul style="list-style-type: none"> <li>i. from the date that point 2 was added to the licence; and</li> <li>ii. from the date that discharge from point 4 commences.</li> </ul>	Section 3.3.1
E3.1	<p>Water Treatment Plant (WTP) Performance Reporting</p> <p>A) The licensee must undertake water quality sampling of all discharges from the WTP (as identified as Point 2 and 4 under condition P1.1) and submit to the EPA a WTP Performance Report within 10 business days of each sample result being taken. Sampling must be undertaken:</p> <ul style="list-style-type: none"> <li>i) daily during discharge</li> <li>ii) as per condition M2.2, following this sampling frequency or as directed by the EPA.</li> </ul>	Not Triggered
<b>Additional Monitoring Conditions</b>		
M4.5	<p>The licensee must undertake monitoring, sampling, video recording and/or take photographs:</p> <ul style="list-style-type: none"> <li>a) if the EPA or licensee reasonably suspects that an event has occurred at the premises or in connection with the carrying out of the activities that has caused, is causing, is likely to cause or has the potential to cause material harm to the environment (whether the harm occurs on or off premises to which the license applies);</li> <li>b) as soon as practicable; and</li> <li>c) as directed by an authorised officer.</li> </ul>	Not triggered

## 3 Monitoring

This section presents summaries of the monitoring completed in the reporting period from 1 November 2025 to 30 November 2025.

Detailed monitoring results for each program are presented in the Appendices.

### 3.1 Weather Monitoring

Meteorological observations were captured using the Bureau of Meteorology Weather Stations - Badgerys Creek (Station 067108). Meteorological data for the month of December can be found within Appendix A.

The total rainfall for this reporting period was 54 mm with 5 days exceeding 1mm, 2 days exceeding 10mm, and 1 day exceeding 20mm of rain.

During the reporting period, 30 days recorded wind gusts greater than 25km/hr, 4 days where the maximum wind gust recorded was greater than 50 km/h, and 1 day where the maximum wind gust recorded was greater than 60 km/hr. Detailed weather observation records for the reporting period are presented in Appendix A.

This information is used daily on site to assess daily activities and consider mitigation measures as required.

TABLE 3 WEATHER SUMMARY AND TRIGGER WEATHER EVENTS FOR REPORTING PERIOD

Weather Event	Observation
Minimum temperature (°C)	8.1
Maximum temperature (°C)	41.9
Total rainfall (mm)	54
Number of days with rain (>1mm)	5
Number of days with rain (>10mm)	2
Number of days with rain (>20mm)	1
Number of days with >25km/h wind gust	30
Number of days with >50km/h wind gust	4
Number of days with >60km/h wind gust	1

### 3.2 Noise and Vibration Monitoring

Noise monitoring is required under Conditions L5.9, L5.10, L5.11, L5.12, L5.13, L5.14 and E1.5 to validate noise predictions for work undertaken outside of standard construction hours in accordance with the construction noise and vibration assessment and monitoring plan. All noise monitoring performed under EPL (21807) will be included in Appendix B.

**TABLE 4 SUMMARY OF NOISE MONITORING FOR REPORTING PERIOD**

<b>Date</b>	<b>Monitoring Location</b>	<b>Attended / Continuous</b>	<b>Description</b>
02/12/2025	51 Kent Road, Orchard Hills	Attended	Residence located opposite Orchard Hills Station
02/12/2025	50 Doncaster Avenue, Claremont Meadows	Attended	Residence located in a quiet neighbourhood, near the M4 highway.
02/12/2025	34 Phillips St, St Marys	Attended	House opposite St Marys Station
10/12/2025	145 Badgerys Creek Road, Bradfield	Attended	Residence west of Bradfield Station
10/12/2025	40 Lansdowne Road, Orchard Hills	Attended	Residence located on a busy intersection.
10/12/2025	8 Cabernet Circuit, Orchard Hills	Attended	Quiet residential area west of the Stabling and Maintenance Facility.
11/12/2025	34 Phillips St, St Marys	Attended	House opposite St Marys Station
13/12/2025	34 Phillips St, St Marys	Attended	House opposite St Marys Station
18/12/2025	40 Lansdowne Road, Orchard Hills	Attended	Residence located on a busy intersection.
16/12/2025	145 Badgerys Creek Road, Bradfield	Attended	Residence west of Bradfield Station
17/12/2025	145 Badgerys Creek Road, Bradfield	Attended	Residence west of Bradfield Station
22/12/2025	40 Lansdowne Road, Orchard Hills	Attended	Residence located on a busy intersection.

## **3.3 Water Monitoring**

### **3.3.1 Surface water monitoring**

As per Condition E2.1 fortnightly sampling is required for at least 3 months from the date Point 2 was added to the licence (30 November 2023). This period ended on 30 February 2024, and additional background monitoring was obtained through March and April. This monitoring is now complete.

Additionally, as per Condition E2.1 surface water monitoring will be conducted at discharge Point 4 at fortnightly intervals and at least once during each discharge event for a minimum of 3 months from the date that discharge from Point 4 commences. These water monitoring results will be presented in Appendix D accordingly.

### **3.3.2 Discharge to water**

The discharge of water from sediment basins occurred at the following discharge point during the reporting period:

- SSTOM-017

The EPL discharge criteria apply to sediment basins identified in condition L2.4 of the approved EPL 21807. Basins and discharge points are summarised in Table 5. Monitoring results for March are included in Appendix C.

TABLE 5 MONITORING/DISCHARGE POINTS AND AREAS

ID	Construction Status	EPA ID	Easting	Northing	Description of location of discharge point	Catchment name	Name of nearest waters	Direct discharge to waters	Date added to EPL
SSTOM-001	Not Active	1	290807.84	6243844.20	The outlet of the sediment basin on the Bradfield site discharging to Thompson Creek	South Creek	Thompsons Creek	Yes	14/11/2023
SSTOM-002	Not Active	2	294041.62	6261905.98	The outlet of the water treatment plant on the St Marys site at former Plaza	South Creek	South Creek	No	15/12/2023
SSTOM-003	Not active	3	291819.86	6258565.85	The outlet of the sediment basin on the Orchard Hills site discharging to an Unnamed Creek (tributary of South Creek)	South Creek	Blaxland Creek	No	14/02/2024
SSTOM-004	Not active	4	291447.72	6243909.96	The outlet of the water treatment plant on the Bradfield site discharging to Thompson Creek	South Creek	Thompsons Creek	No	15/05/2024
SSTOM-005	Not active	5	292112.47	6257621.18	The outlet of the sediment basin at the Stabling and Maintenance Facility site discharging to Blaxland Creek	South Creek	Blaxland Creek	No	28/08/2024
SSTOM-006	Not active	6	291092.66	6252180.95	The outlet of the sediment basin discharging to Cosgroves Creek	South Creek	Cosgrove Creek	No	04/09/2024
SSTOM-007	Not active	7	292065.7	6259303.9	The outlet of the sediment basin discharging to South Creek	South Creek	South Creek	No	15/11/2024
SSTOM-008	Not active	8	291981.6	6249912.7	The outlet of the sediment basin discharging to Badgerys Creek	Badgerys Creek	Badgerys Creek	No	4/12/2024
SSTOM-009	Not active	9	291981.6	6249912.7	The outlet of the sediment basin discharging to Claremont Creek	South Creek	Claremont Creek	No	16/01/2025
SSTOM-010	Not active	10	292018.2	6261255.3	The outlet of the sediment basin discharging to Claremont Creek	South Creek	Claremont Creek	No	16/01/2025

SSTOM-011	Not active	11	291965.4	6258444.4	The outlet of the sediment basin discharging to Badgerys Creek	South Creek	Badgerys Creek	No	16/01/2025
SSTOM-012	Not Active	12	291985.4	6257951.5	The outlet of the sediment basin discharging to Blaxland Creek	South Creek	Blaxland Creek	Yes	16/01/2025
SSTOM-013	Not Active	13	291528.1	6255484.1	The outlet of the sediment basin located south of Patons Lane to Unnamed Creek	South Creek	Unnamed Creek	No	23/01/2025
SSTOM-014	Not Active	14	289482.8	6245852.0	The outlet of the sediment basin at the Bringelly site discharging to Badgerys Creek.	South Creek	Badgerys Creek	Yes	23/01/2025
SSTOM-015	Not active	15	290913.5	6253487.3	The outlet of the sediment basin near Luddenham Station discharging to an unnamed tributary of South Creek	South Creek	South Creek	No	25/03/2025
SSTOM-016	Not Active	16	291749.9	6257486.0	The outlet of the sediment basin near Linewide (South Lansdown Road) Station discharging to Blaxland Creek	South Creek	Blaxland Creek	No	4/06/2025
SSTOM-017	Actvie	17	290808.06	6243841.41	The outlet of the sediment basin on the Bradfield site discharging to Thompson Creek referred to in Condition P1.2	South Creek	Thompson Creek	Yes	14/10/2025



## Appendices



## Appendix A Weather Observations

TABLE 6 MONTHLY WEATHER OBSERVATION TABLE

Date	Temperature		Rainfall	Wind Observations			Morning (9am) Weather Observation					Afternoon (3pm) Weather Observation				
	Minimum (°C)	Maximum (°C)	In the 24 hours to 9am (mm)	Direction of maximum wind gust	Speed of maximum wind gust (km/h)	Time of maximum wind gust	Temperature (°C)	9am relative humidity (%)	Wind direction	Wind speed (km/h)	9am MSL pressure (hPa)	Temperature (°C)	3pm relative humidity (%)	Wind direction	Wind speed (km/h)	3pm MSL pressure (hPa)
1	8.1	25.1	0	NW	52	14:52	20.1	34	NW	13	1006.4	22.2	26	NW	31	1002.8
2	10.9	25.3	0	SW	43	8:17	16.1	45	WSW	26	1010	22.2	36	ESE	13	1011.9
3	9.1	31.2	0	E	30	14:09	21.2	45	N	11	1019.6	28.8	25	ESE	6	1015.5
4	11.5	36	0	ENE	37	16:27	23.4	46	N	4	1018.6	34.7	15	NE	13	1012.4
5	11.7	40.3	0	ENE	35	16:52	25.9	37	NNE	7	1014	38.4	11	NE	6	1009.1
6	14.6	41.9	0	W	93	17:33	27.1	37	E	6	1008	38.9	15	N	20	1000.4
7	21.2	25.3	0	E	37	15:06	23.8	41	SSW	17	1008.2	19.9	59	ESE	15	1012
8	15.2	31.3	0	NNE	46	11:36	20	70	N	9	1015.2	30.2	37	NE	11	1009.7
9	15.2	37.5	0	ESE	41	14:49	31.8	22	NNW	6	1012.3	33.4	20	ESE	28	1010.4
10	18.6	30	0	ESE	30	17:36	21	61	S	6	1021.2	27.3	53	E	17	1015.4
11	17.1	24.2	8.4	SSE	35	12:42	20.8	71	S	13	1020.6	21.6	63	SE	17	1020.3
12	17.2	24.6	21	SE	33	13:14	18.7	99	SE	9	1017.8	22.6	64	ESE	19	1016
13	14.4	30.7	8.8	SSW	26	15:28	18.9	87	NNE	7	1012.8	28.9	41	NE	7	1006.8
14	17.5	34.5	12	WNW	46	15:54	22	78	NNE	4	1005.9	33.9	31	W	24	1001.6
15	16.4	27.3	0	E	35	13:35	21.4	65	SE	7	1013.9	23.6	54	ESE	24	1013
16	15.5	22.3	0.4	E	20	15:54	18.4	78	SSW	4	1022.5	20.7	62	SE	6	1022.2
17	14.5	31.2	0	E	31	16:31	19.6	77	NNE	4	1024.2	28.6	47	NE	9	1020.1
18	15.8	39.2	0	NE	33	17:39	23.8	68	NE	4	1017.8	36.1	35	NNE	11	1012.3
19	18.1	41.6	0	SSW	56	13:09	30.8	45	N	4	1010.3	32.5	35	NNE	30	1006
20	20.8	33.9	3	SSW	33	22:48	23.9	82	NNE	11	1008.8	33.8	45	N	17	1003.9
21	21.5	38.7	0.2	WNW	54	19:13	32.1	48	NNE	9	1004	36.8	32	SW	9	1001
22	21.8	34.1	0.2	NNW	46	23:23	24.7	47	WSW	11	1006.2	26	57	SE	24	1005.7
23	16.8	33.3	0	ESE	43	15:01	23.9	65	S	4	1008.6	32.3	21	SSW	24	1007.1
24	15.4	35.6	0	SSE	39	21:04	21	65	N	9	1012	34.4	19	N	7	1005.1
25	16.5	25.7	0	SE	41	14:08	21.8	62	SE	6	1011.1	22.8	47	ESE	24	1009.8
26	13.7	18.7	0	SW	31	8:53	14.3	62	SE	15	1015.5	17.8	49	SE	7	1015.4
27	11.3	25.2	0	ENE	33	14:13	19.4	47	SSW	7	1017.3	21.7	41	E	17	1014.5
28	12.3	25	0	SE	33	15:47	18.3	48	SSW	17	1020.3	22.9	40	SSE	15	1020.3
29	10.4	27.5	0	E	35	14:53	20	51	S	6	1021.3	25.9	36	E	22	1017.4
30	11.1	30.1	0	NE	28	13:45	19.2	57	NNE	6	1015.5	29.1	32	ENE	17	1009.4
31	11.9	27	0	ESE	39	18:17	20.5	63	SSE	7	1011	23.6	50	ENE	19	1007.5

## Appendix B Noise Monitoring

TABLE 7 DETAILED NOISE MONITORING DATA

Date	Time	Construction Activity	Activity Location	Monitoring Location	NML (dBA)	Predicted (dBA)	Recorded LA <sub>eq(15min)</sub> (dBA)	LA <sub>Max</sub>	LA <sub>10</sub>	LA <sub>90</sub>	Exceedance of Predicted (dBA)	Exceedance of Predicted	Comments
02/12/2025	08:09	Concrete Crusher	Orchard Hills Station	51 Kent Road, Orchard Hills	54	69	65	83.5	69	53.5	-4	No	Dominant noise source was local traffic. PLM works only faintly audible during brief breaks in traffic, with measured noise levels remaining below those predicted by DNVIS.
02/12/2025	14:08	Concrete Crusher	Orchard Hills Station	50 Doncaster Avenue, Claremont Meadows	47	68	47.1	66.3	48.2	42.3	-20.9	No	Dominant noise source was local traffic. PLM works only faintly audible during brief breaks in traffic, with measured noise levels remaining below those predicted by DNVIS.
02/12/2025	23:11	Utility Investigation	St Marys Station	34 Phillips St, St Marys	41	71	55.8	75.3	59.3	42.4	-15.2	No	Dominant noise source was local traffic. PLM works only faintly audible during brief breaks in traffic, with measured noise levels remaining below those predicted by DNVIS.
10/12/2025	20:01	Concrete Pour	Bradfield Station	145 Badgerys Creek Road, Bradfield	40	47	42.9	70.3	45.2	36	-4.1	No	PLM works audible, with measured noise levels remaining below those predicted by DNVIS.
10/12/2025	22:30	Blockwork / FRP	Orchard Hills Station	40 Lansdowne Road, Orchard Hills	45	53	47.7	67.4	48.3	37.6	-5.3	No	Dominant noise sources were local traffic, birds, insects and planes. PLM works only faintly audible during brief breaks in traffic, with measured noise levels remaining below those predicted by DNVIS.
10/12/2025	23:06	CSR	Stabling and Maintenance Facility	8 Cabernet Circuit, Orchard Hills	45	55	37.3	52.3	40.1	33.8	-17.7	No	PLM works audible, with measured noise levels remaining below those predicted by DNVIS.

Date	Time	Construction Activity	Activity Location	Monitoring Location	NML (dBA)	Predicted (dBA)	Recorded LAeq(15min) (dBA)	LAmx	LA <sub>10</sub>	LA <sub>90</sub>	Exceedance of Predicted (dBA)	Exceedance of Predicted	Comments
11/12/2025	00:02	Pre-cast Install	St Marys Station	34 Phillips St, St Marys	41	59	47.2	70.6	47.3	37.9	-11.8	No	PLM works audible, with measured noise levels remaining below those predicted by DNVIS.
13/12/2025	13:23	Utility Investigation	St Marys	34 Phillips St, St Marys	42	71	63.8	83.3	66.7	53.8	-7.2	No	Dominant noise source was local traffic. PLM works inaudible.
18/12/2025	22:30	Escalator Install	Orchard Hills Station	40 Lansdowne Road, Orchard Hills	45	49	45.5	59.6	48.4	42.2	-3.5	No	Dominant noise sources were local traffic, birds, insects and planes. PLM works only faintly audible during brief breaks in traffic, with measured noise levels remaining below those predicted by DNVIS.
16/12/2025	20:25	Station box fitout	Bradfield Station	145 Badgerys Creek Road, Bradfield	40	42	39.2	67.3	39	36.6	-2.8	No	PLM works audible, with measured noise levels remaining below those predicted by DNVIS.
17/12/2025	21:46	Station box fitout	Bradfield Station	145 Badgerys Creek Road, Bradfield	40	42	41.8	49.6	42.7	40.8	-0.2	No	Dominant noise source was insects. PLM works only periodically audibl, with measured noise levels remaining below those predicted by DNVIS.
22/12/2025	06:18	Boral batch plant	Orchard Hills Station	40 Lansdowne Road, Orchard Hills	45	45	56.4	80.4	57.8	45.6	11.4	Yes	Dominant noise source was local traffic and power tools from being used in a nearby residential property. PLM works only faintly audible during brief breaks in traffic, with measured noise levels remaining below those predicted by DNVIS.

## Appendix C      Discharge to water

TABLE 8 WATER DISCHARGE TABLE

Discharge Monitoring Point ID	Type of Monitoring Point	Type of Discharge Point	Date	Discharge Permit No.	Oil and Grease (Visual Inspection)	pH (6.5-8.5)	Turbidity (50 NTU)
SSTOM-017	Sediment Basin	Discharge into stabilised spillway	19/12/2026	PMJV-ENV-DWP-127	Not Visible	6.93	5.9


---

## Appendix D    Surface water monitoring

No surface water monitoring was conducted for this month's monitoring report. Any surface water monitoring conducted as part of Parklife Metro's EPL licence will be presented accordingly.

---

## **Appendix E      Premise Maps – December**

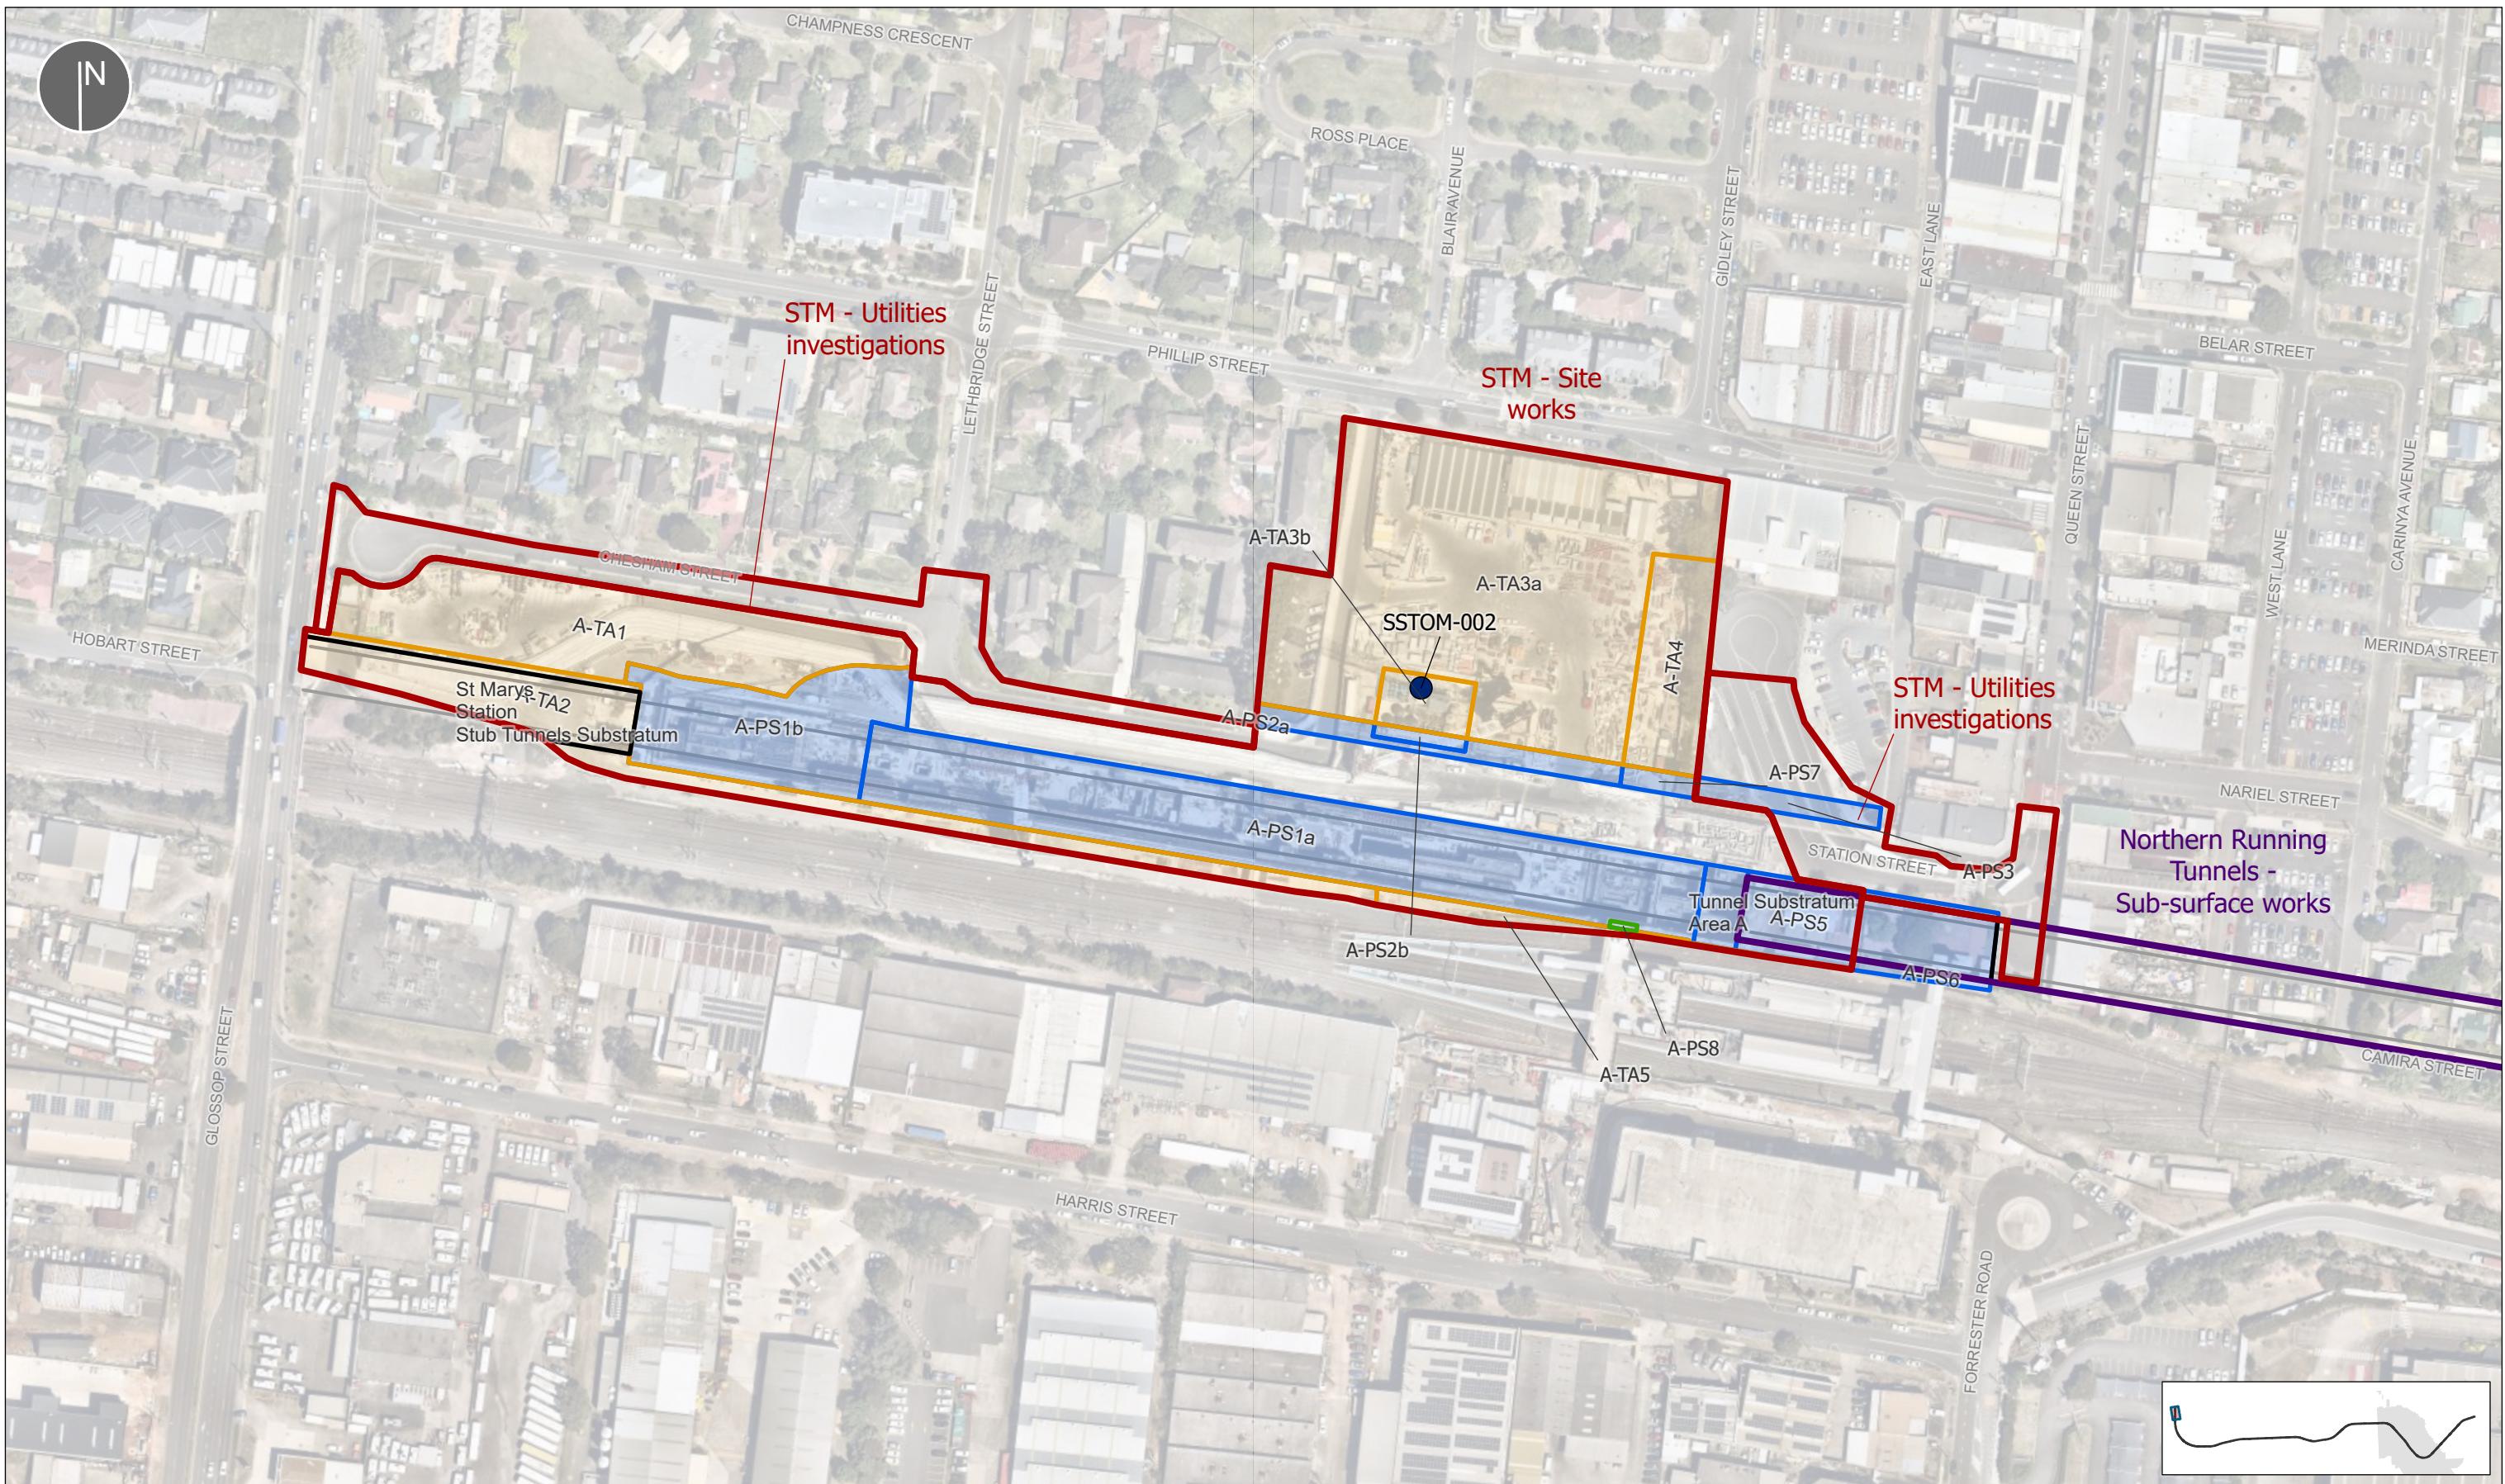

LEGEND	
Discharge Points	EPL Premise Boundary
Water Treatment Plant	Surface works
	Sub-surface works
Metro alignment	Site Access Schedule
Watercourse	Aerial Stratum
Western Sydney International boundary (WSP)	Project Site
	Substratum

Temporary Area



NOTES  
EPL Premise Boundary Map

REV	DATE	DESCRIPTION
43	08.10.2025	Premise Map update
44	28.10.2025	Premise Map update
45	04.11.2025	Premise Map update
46	17.11.2025	Premise Map update
47	05.12.2025	Premise Map update
48	16.01.2026	Premise Map update

TITLE  
EPL 21807 PREMISE BOUNDARY

SCALE  
1:2,000

0 40 80m

PROJECT  
Sydney Metro – Western Sydney Airport - SSTOM


CLIENT  
Sydney Metro


MAP #  
SMWSASSM-PLD-1NL-ENV-GIS-000001\_48

PROJECT  
Sydney Metro – Western Sydney Airport - SSTOM

CLIENT  
Sydney Metro

MAP #  
SMWSASSM-PLD-1NL-ENV-GIS-000001\_48

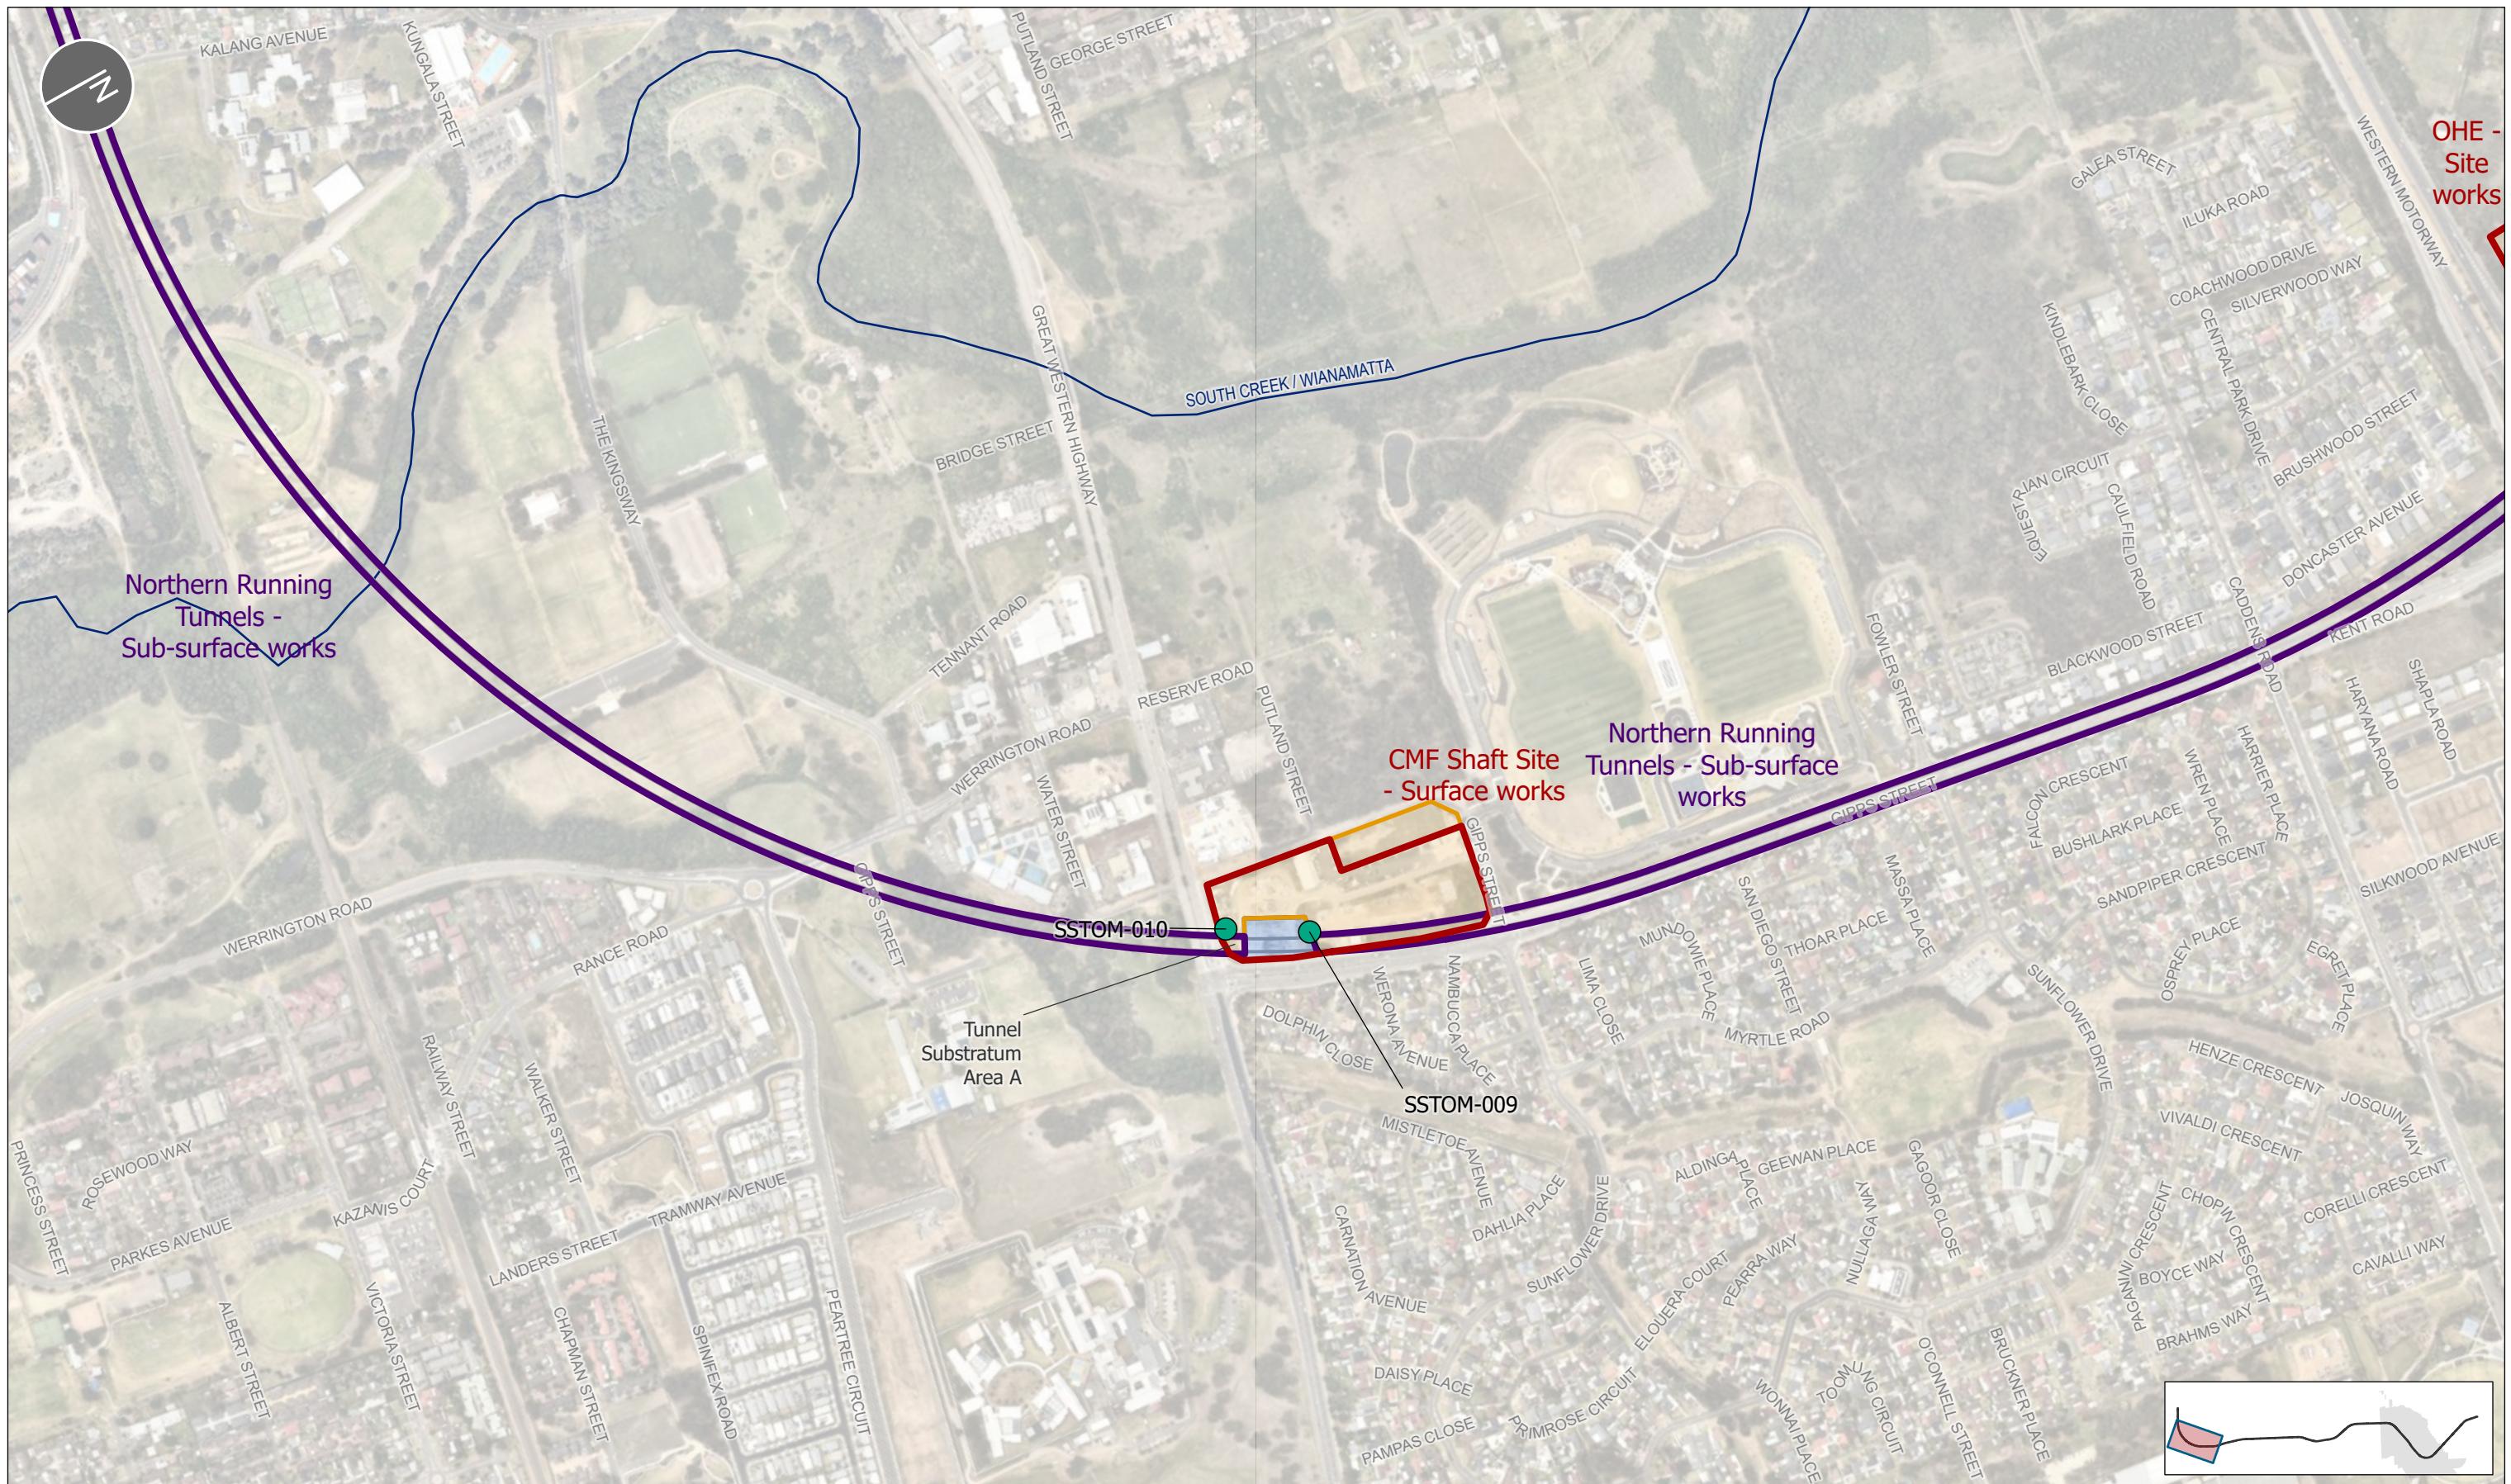

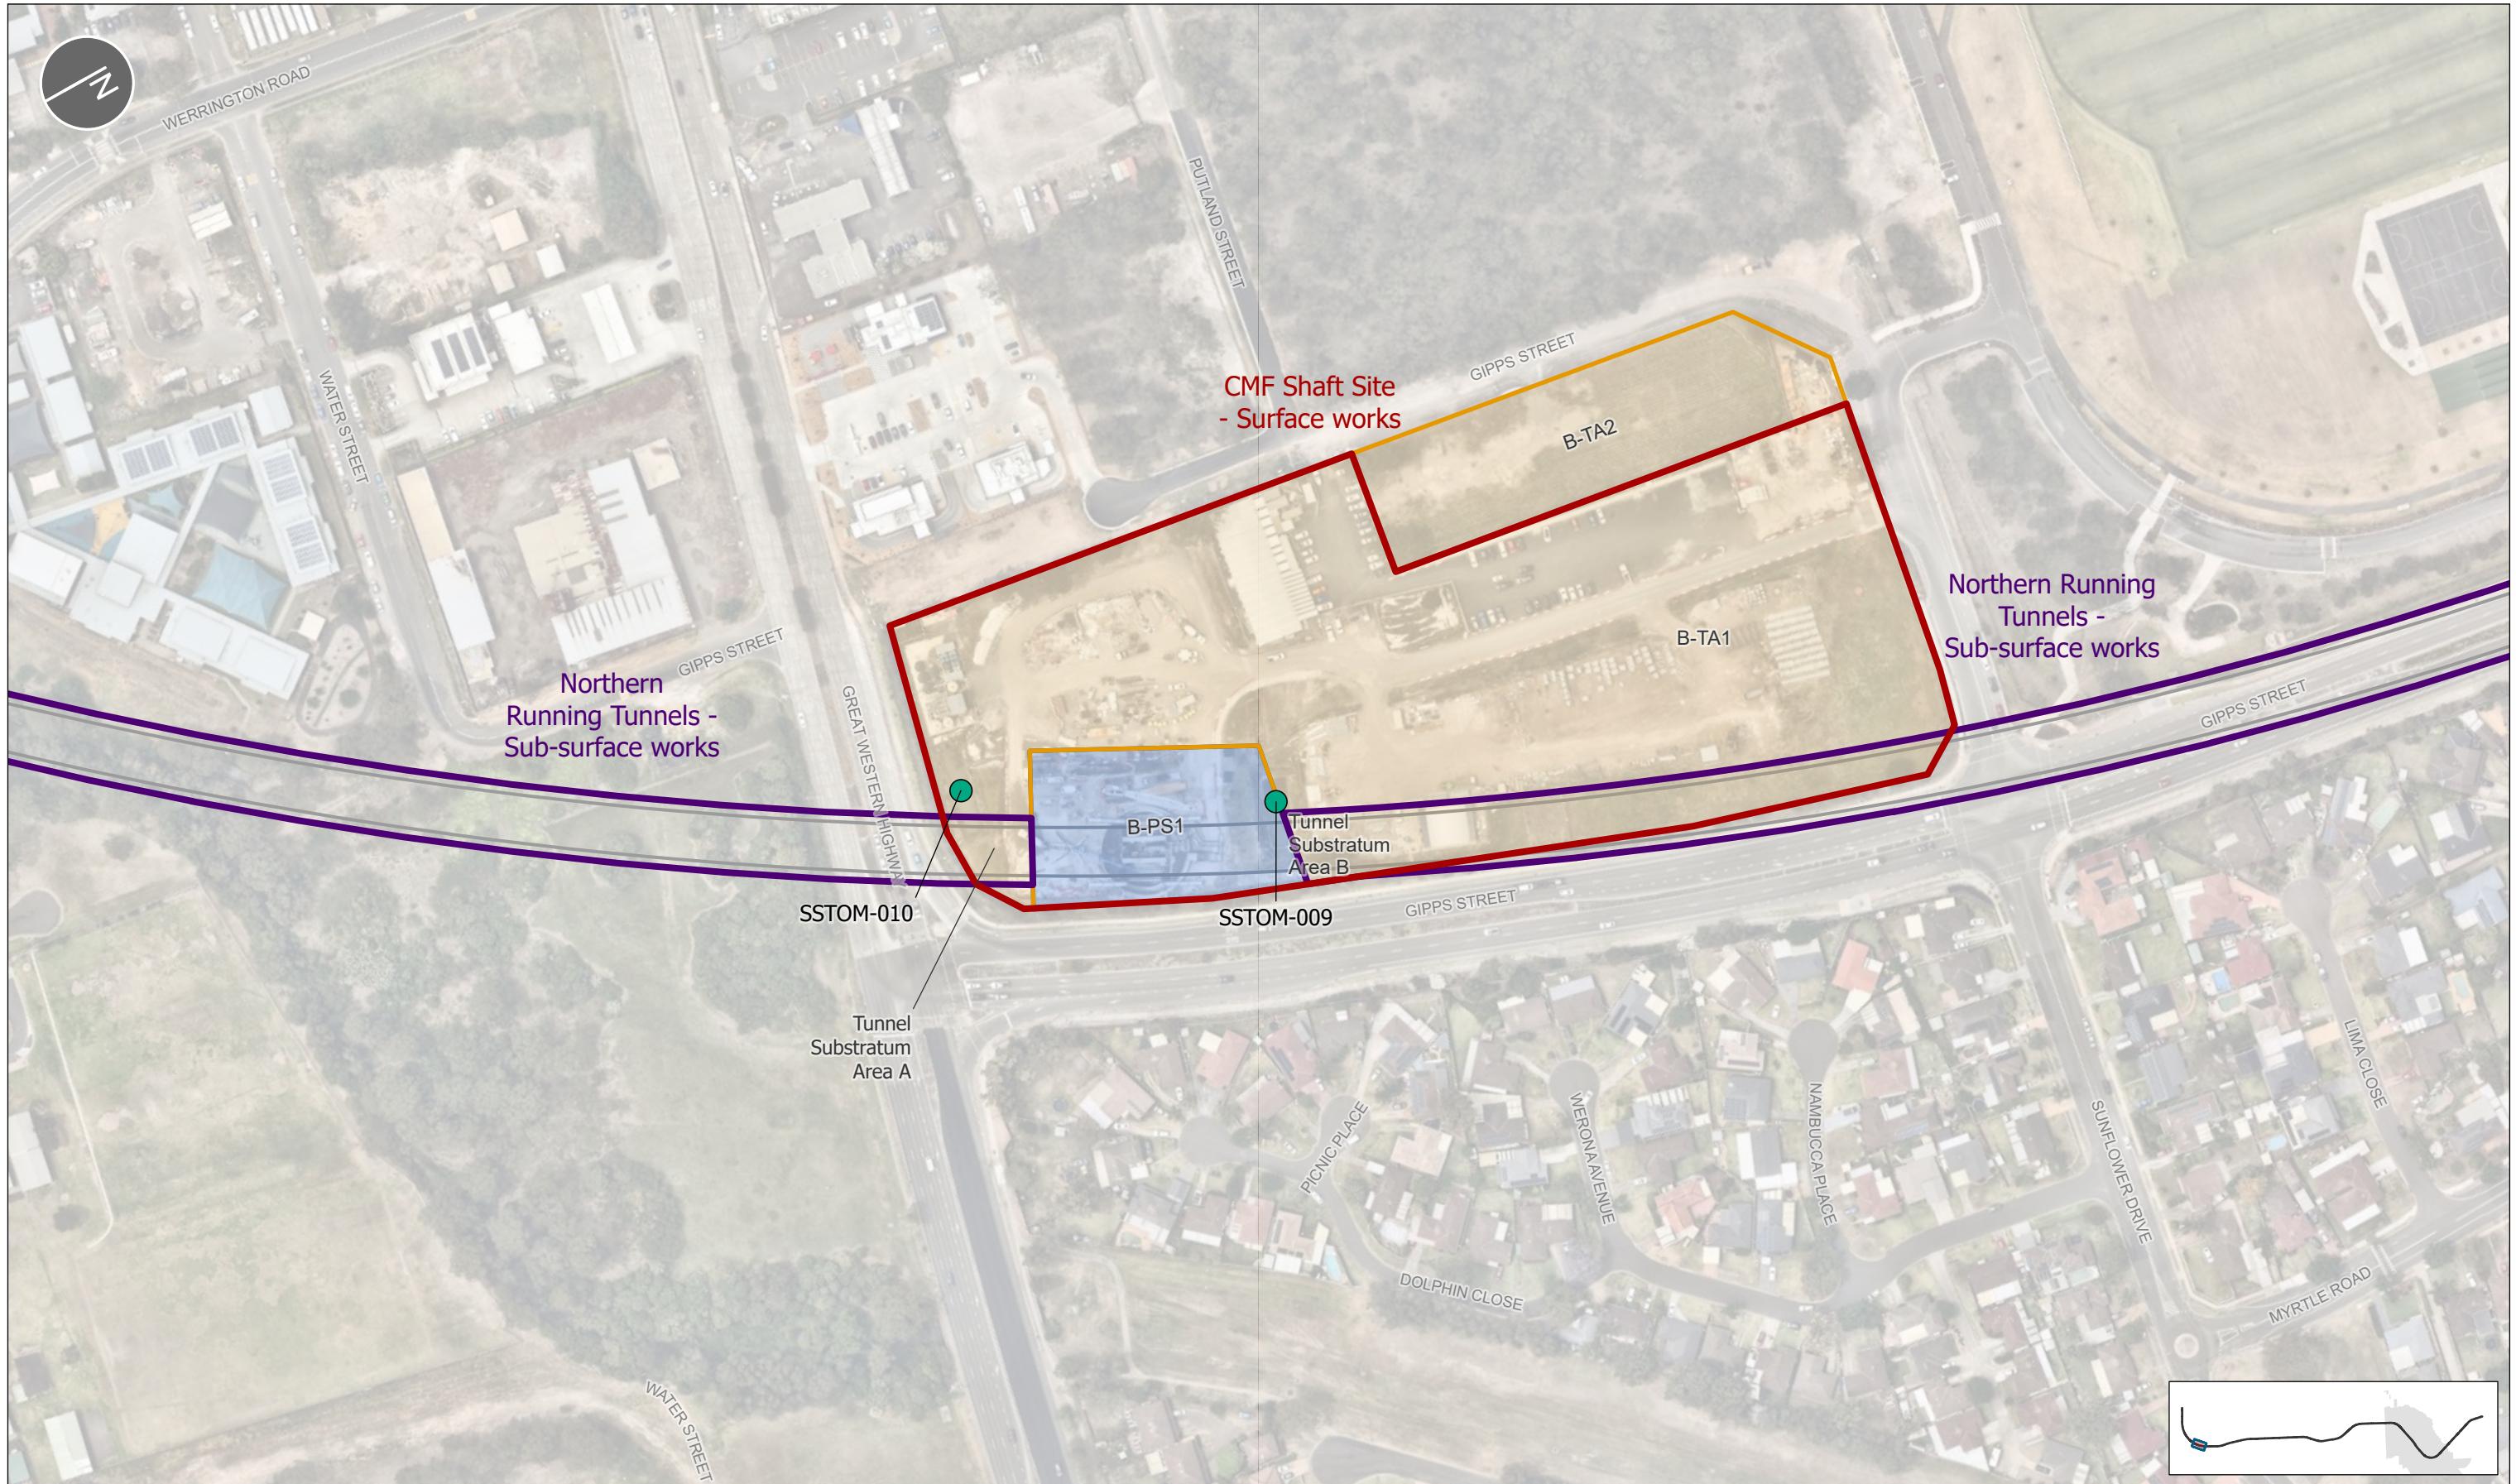

**LEGEND**

<b>Discharge Points</b>	<b>EPL Premise Boundary</b>	<b>Metro alignment</b>	<b>Site Access Schedule</b>	<b>NOTES</b>	<b>REV</b>	<b>DATE</b>	<b>DESCRIPTION</b>
				EPL Premise Boundary Map	43	08.10.2025	Premise Map update
<b>Temporary Sediment Basin</b>					44	28.10.2025	Premise Map update
					45	04.11.2025	Premise Map update
					46	17.11.2025	Premise Map update
					47	05.12.2025	Premise Map update
					48	16.01.2026	Premise Map update

**Discharge Points**

**EPL Premise Boundary**

**Metro alignment**

**Site Access Schedule**

**Project Site**

**Surface works**

**Substratum**

**Sub-surface works**

**Watercourse**

**Western Sydney International boundary (WSP)**

**Temporary Area**

**NOTES**

**REV**

**DATE**

**DESCRIPTION**

**TITLE**  
EPL 21807 PREMISE BOUNDARY

**PROJECT**  
Sydney Metro – Western Sydney Airport - SSTOM

**CLIENT**  
Sydney Metro

**SCALE**  
1:2,000

**A3**

**BY**

**ROVED**

**MAP #**  
SMWSASSM-PLD-1NL-ENV-GIS-000001\_48

**REV**

**0** **40** **80m**


**SHEET**  
3 of 12

**COORDINATE SYSTEM**  
GDA2020 MGA Zone 56

**NEW**

**DATE**  
16/01/2026

**48**

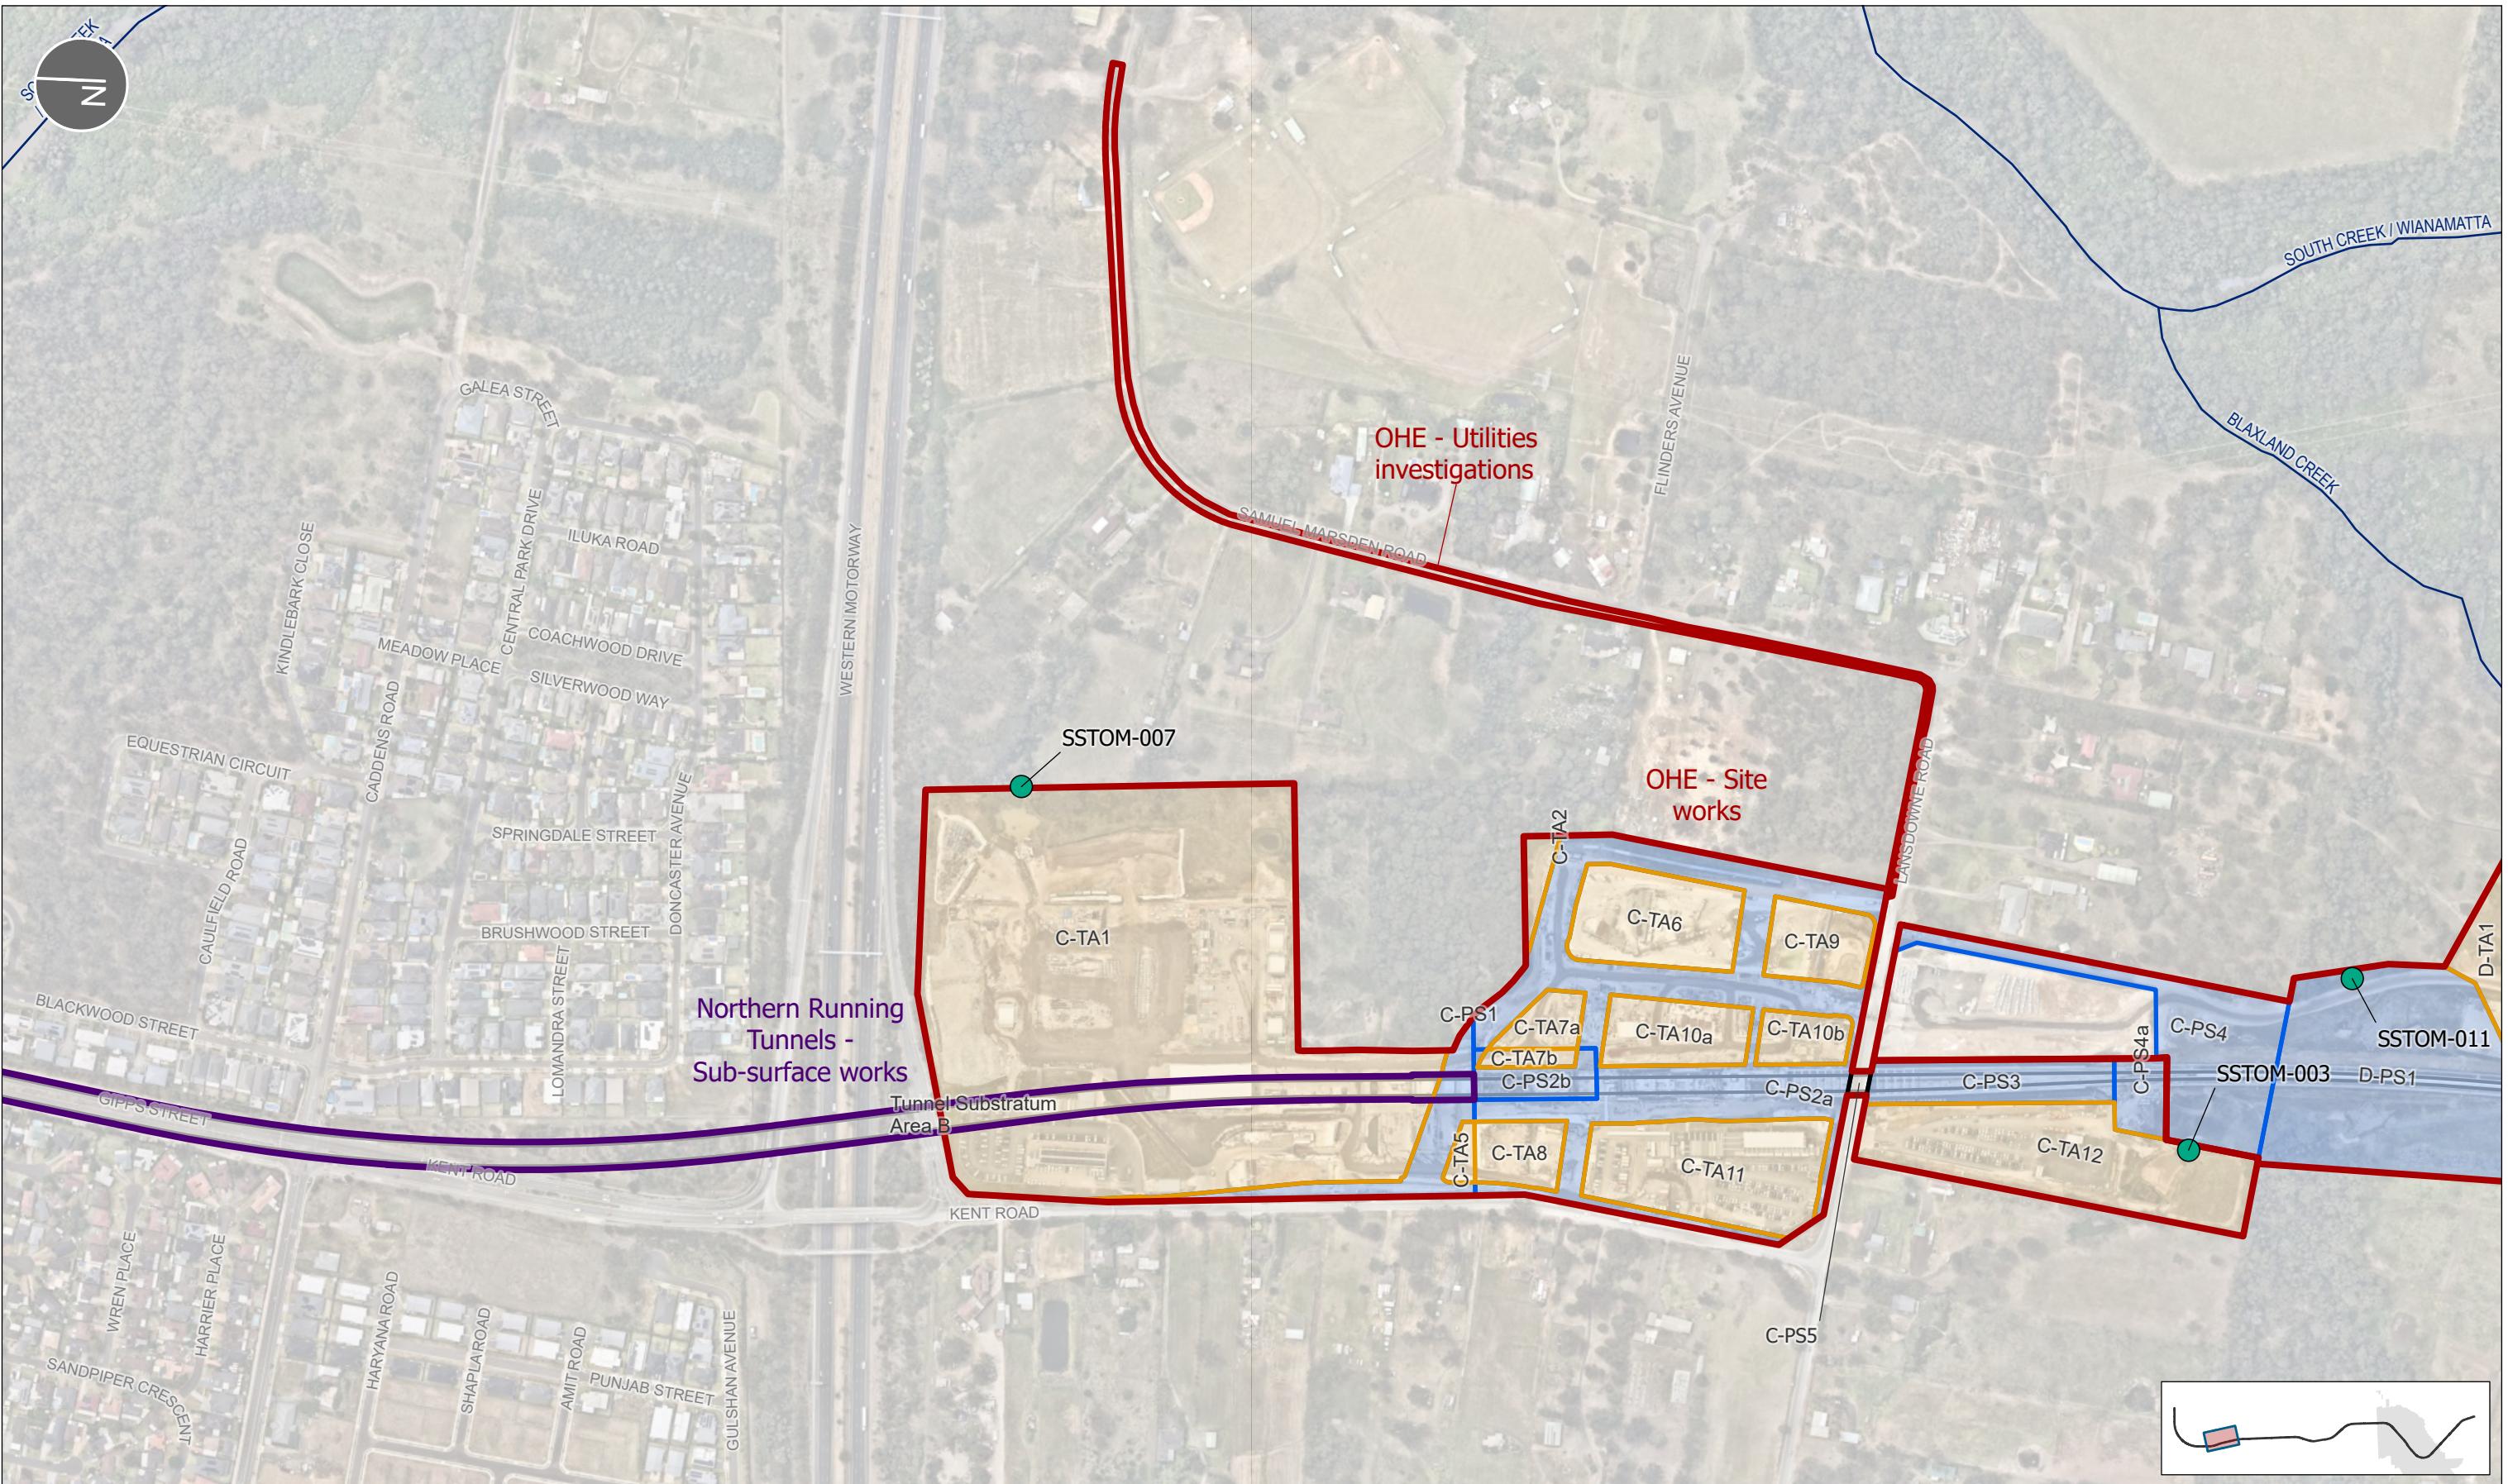

LEGEND

Discharge Points  
Temporary Sediment Basin

EPL Premise Boundary  
Surface works  
Sub-surface works

Metro alignment  
Watercourse  
Western Sydney International boundary (WSP)

Site Access Schedule  
Project Site  
Substratum  
Temporary Area



NOTES  
EPL Premise Boundary Map

REV	DATE	DESCRIPTION
43	08.10.2025	Premise Map update
44	28.10.2025	Premise Map update
45	04.11.2025	Premise Map update
46	17.11.2025	Premise Map update
47	05.12.2025	Premise Map update
48	16.01.2026	Premise Map update

TITLE  
EPL 21807 PREMISE BOUNDARY

SCALE  
1:5,000

0 100 200m

PROJECT  
Sydney Metro – Western Sydney Airport - SSTOM

CLIENT  
Sydney Metro

MAP #  
SMWSASSM-PLD-1NL-ENV-GIS-000001\_48

REV


4 of 12


DATE  
16/01/2026


COORDINATE SYSTEM  
GDA2020 MGA Zone 56

BY  
ROVED


EW

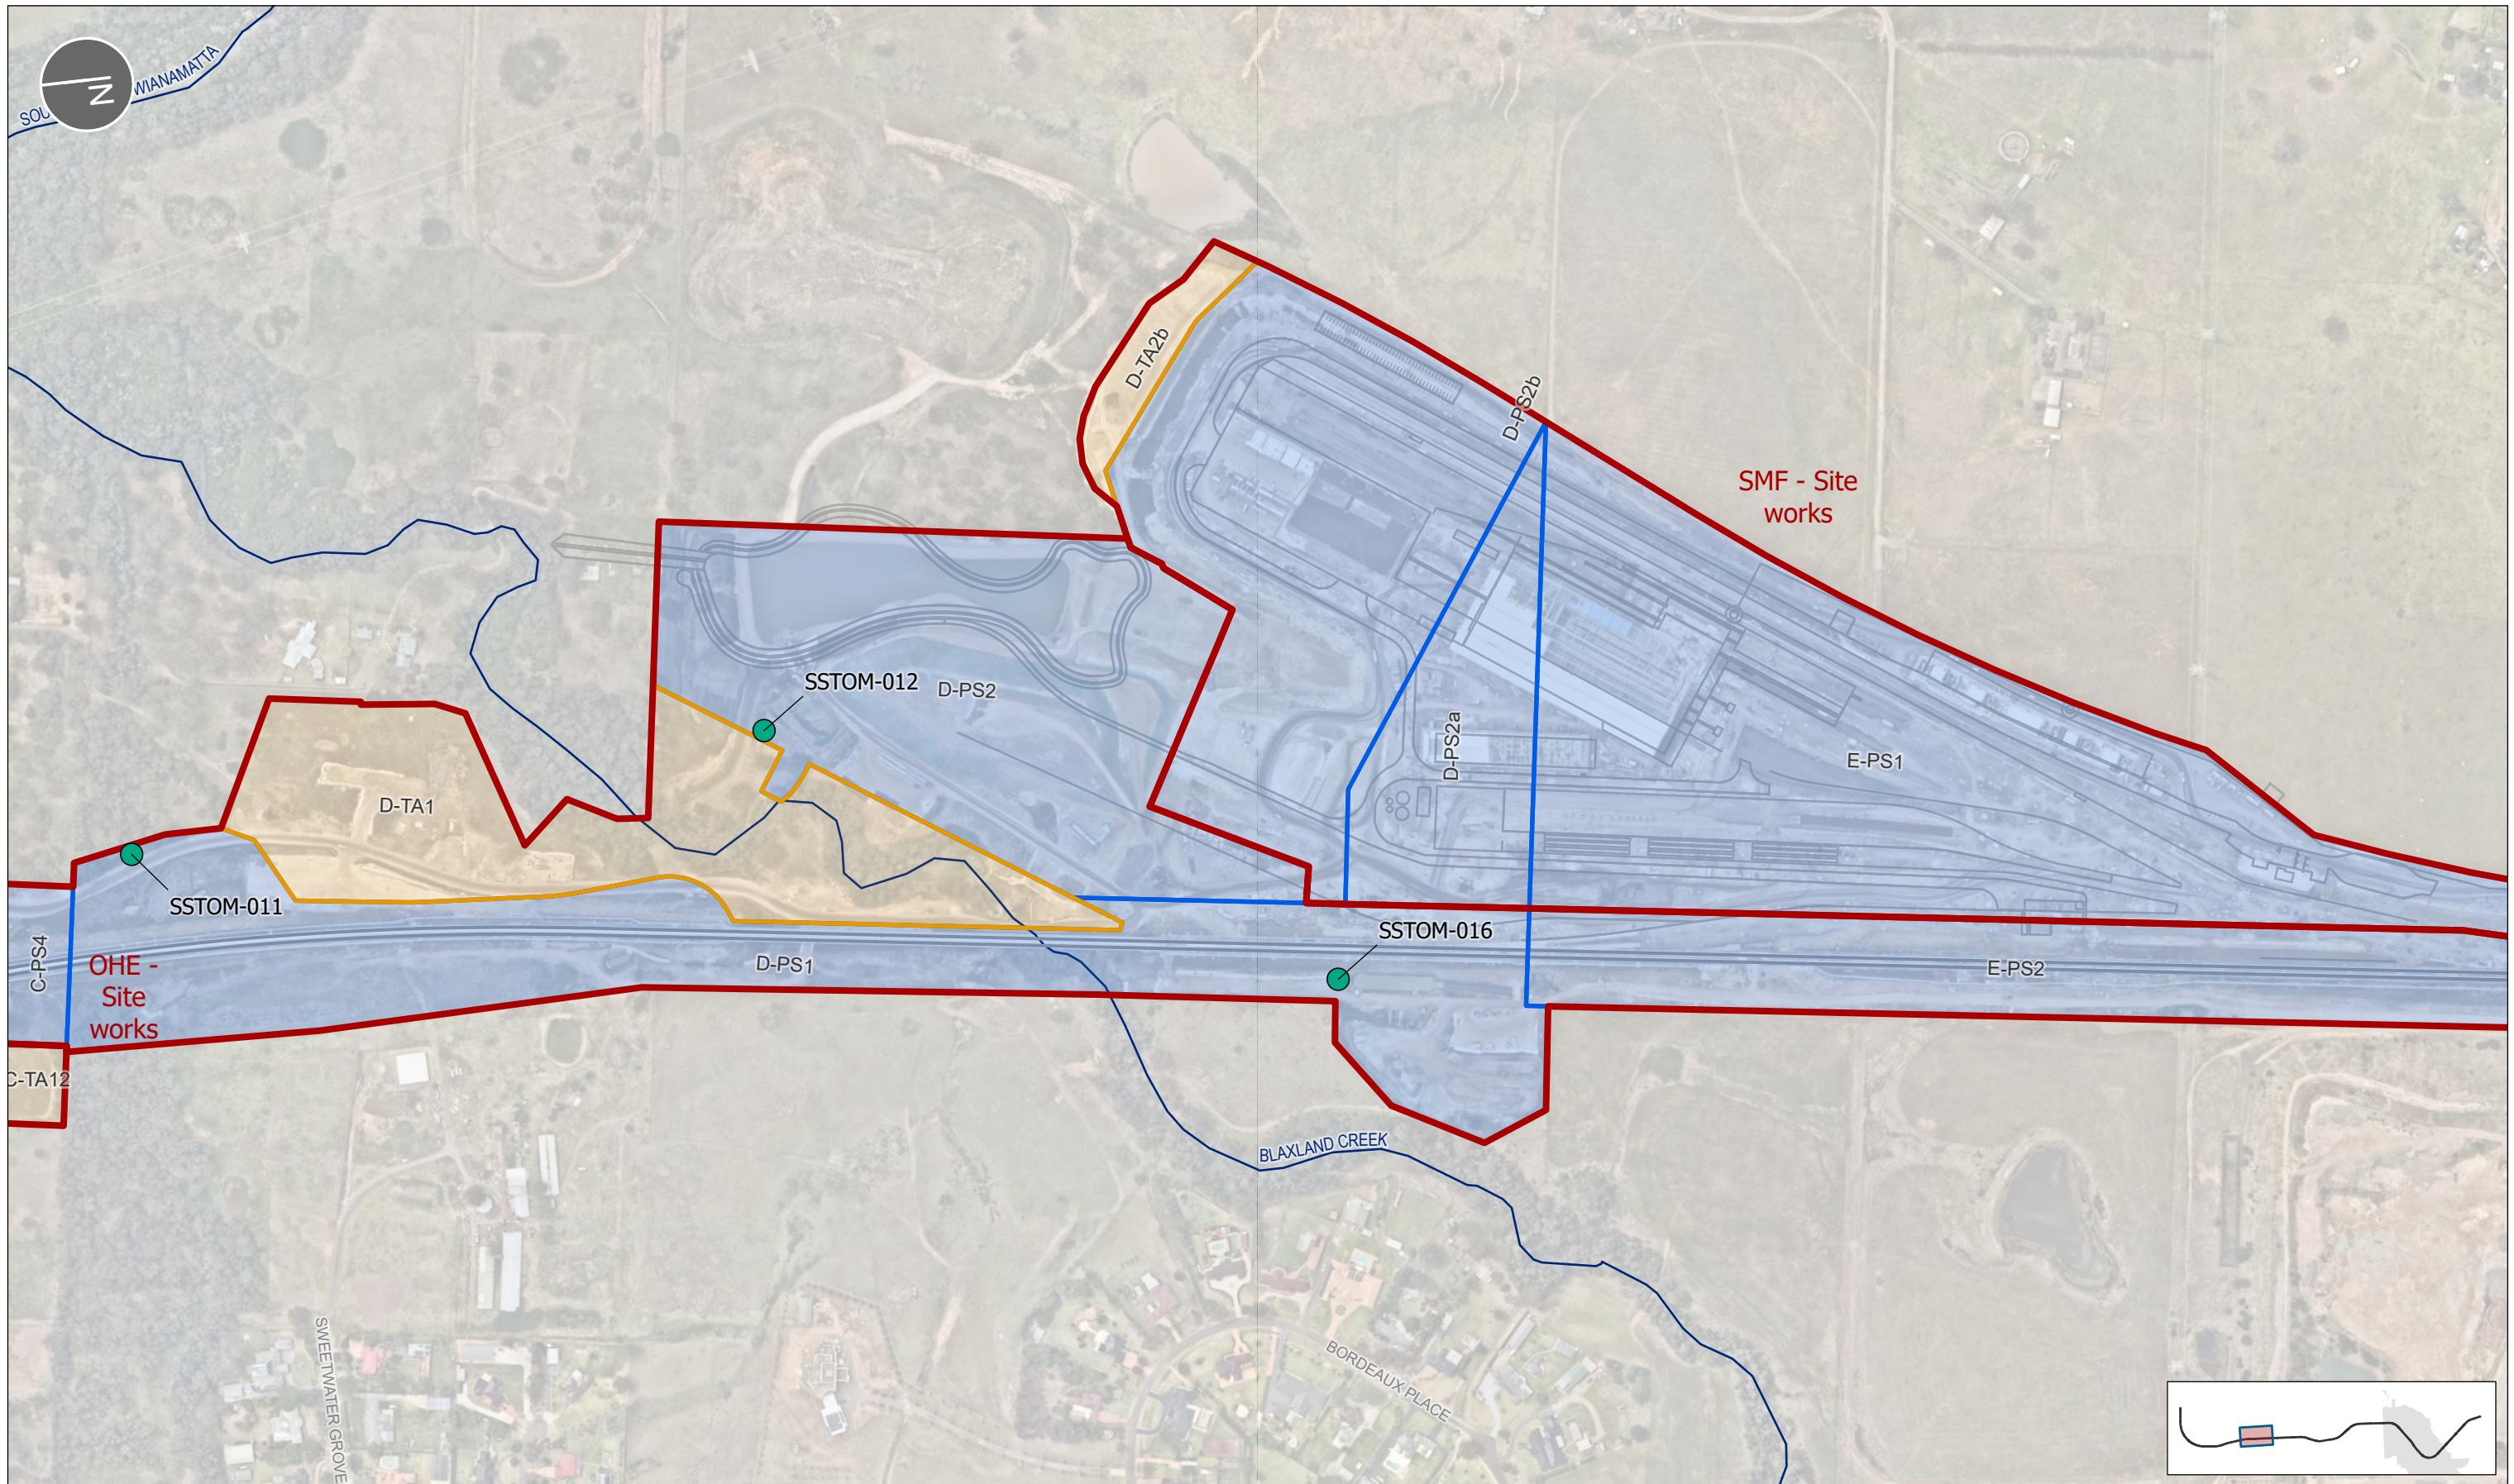

LEGEND		NOTES		REV	DATE	DESCRIPTION
Discharge Points	EPL Premise Boundary	Metro alignment	EPL Premise Boundary Map	43	08.10.2025	Premise Map update
Temporary Sediment Basin	Surface works	Watercourse		44	28.10.2025	Premise Map update
	Sub-surface works	Western Sydney International boundary (WSP)		45	04.11.2025	Premise Map update
		Site Access Schedule		46	17.11.2025	Premise Map update
		Project Site		47	05.12.2025	Premise Map update
		Temporary Area		48	16.01.2026	Premise Map update
		<b>EPL 21807 PREMISE BOUNDARY</b> <b>PROJECT</b> <b>Sydney Metro – Western Sydney Airport - SSTOM</b>		CLIENT	Sydney Metro	
		SCALE	1:5,000	A3	BY	ROVED
SHEET 5 of 12		COORDINATE SYSTEM	GDA2020 MGA Zone 56	NEW	DATE	MAP # SMWSASSM-PLD-1NL-ENV-GIS-000001_48
GIS MAP file: SSTOM_ENV_EPL   C:\Live_Projects\sstom_gis\current\maps\Environment\SSTOM_ENV_EPL.aprx						

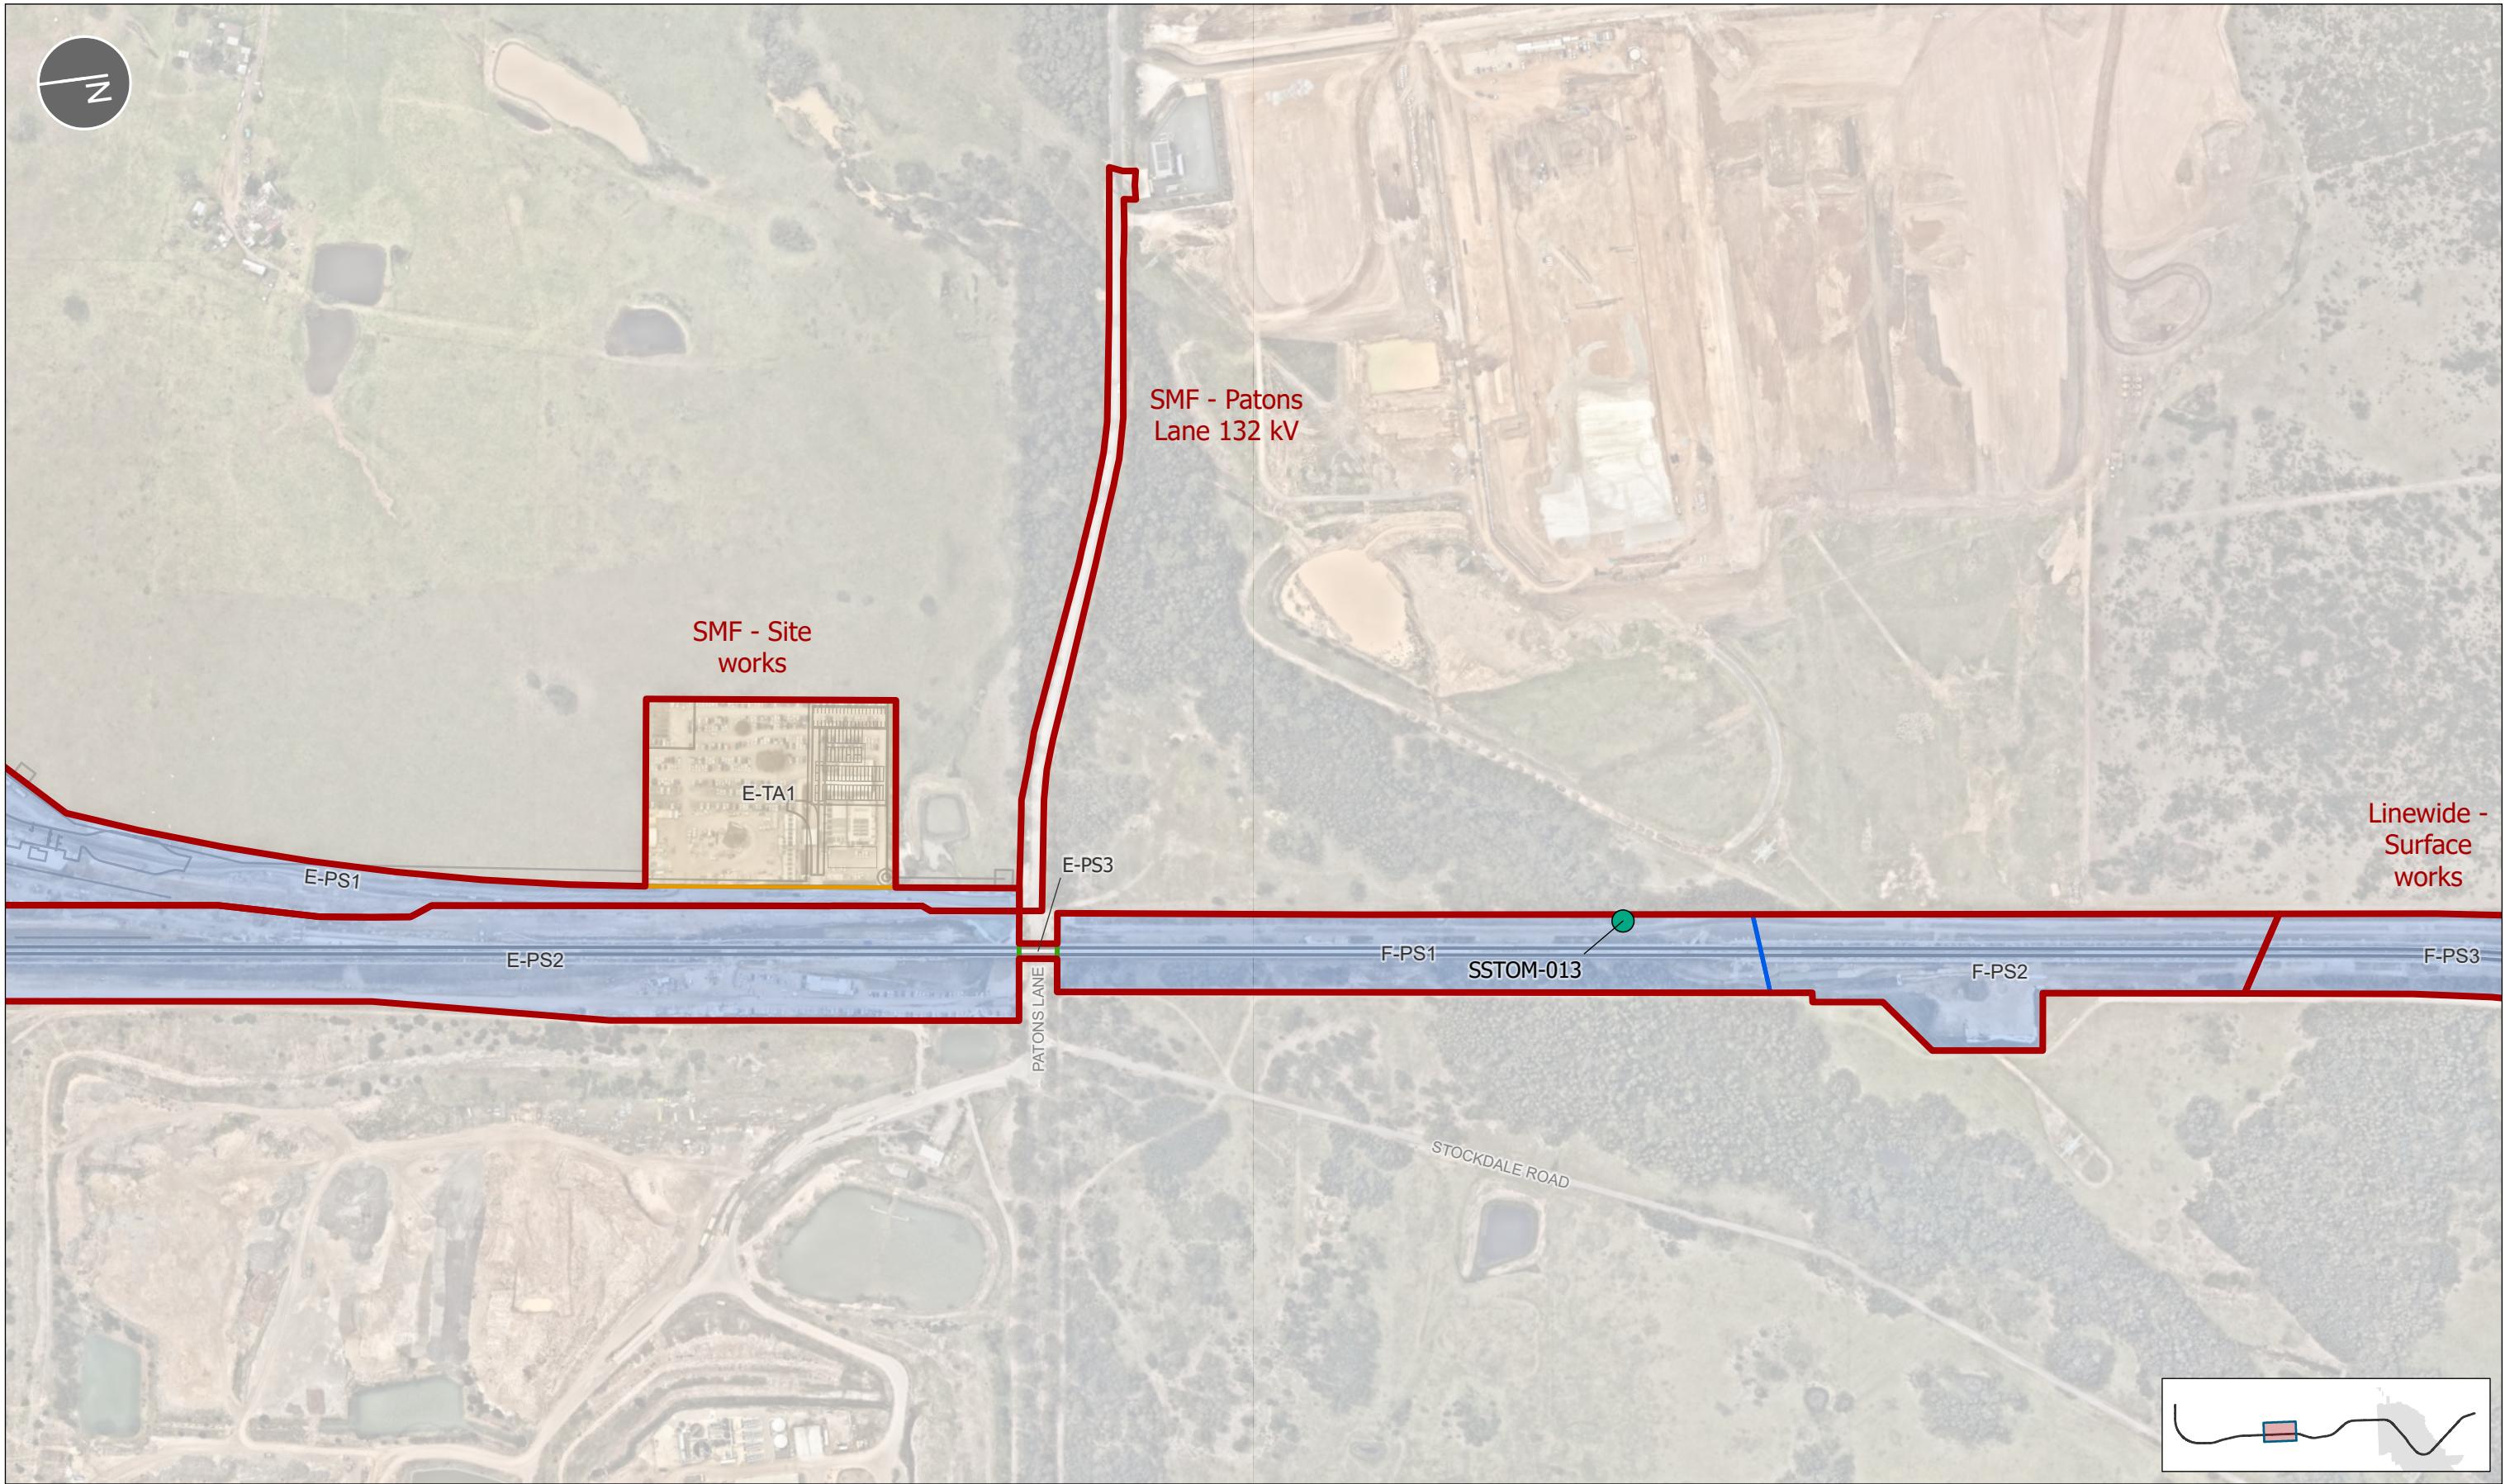

LEGEND	NOTES	REV	DATE	DESCRIPTION
<b>Discharge Points</b> <span style="color: green;">●</span> Temporary Sediment Basin	EPL Premise Boundary Map	43	08.10.2025	Premise Map update
<b>EPL Premise Boundary</b> <span style="color: red;">■</span> Surface works		44	28.10.2025	Premise Map update
<span style="color: grey;">—</span> Metro alignment <span style="color: blue;">—</span> Watercourse <span style="color: purple;">■</span> Sub-surface works		45	04.11.2025	Premise Map update
<span style="color: black;">■■■</span> Site Access Schedule <span style="color: green;">■</span> Aerial Stratum <span style="color: blue;">■</span> Project Site <span style="color: yellow;">■</span> Temporary Area		46	17.11.2025	Premise Map update
<span style="color: black;">■■■</span> Western Sydney International boundary (WSP)		47	05.12.2025	Premise Map update
		48	16.01.2026	Premise Map update
	<b>Parklife Metro D&amp;C</b>			
	<b>EPL 21807 PREMISE BOUNDARY</b>			
	PROJECT Sydney Metro – Western Sydney Airport - SSTOM			CLIENT Sydney Metro
	SCALE 1:5,000	A3	BY ROVED	MAP # SMWSASSM-PLD-1NL-ENV-GIS-00001_48
	0 100 200m			REV
	SHEET 6 of 12	COORDINATE SYSTEM GDA2020 MGA Zone 56	DATE 16/01/2026	

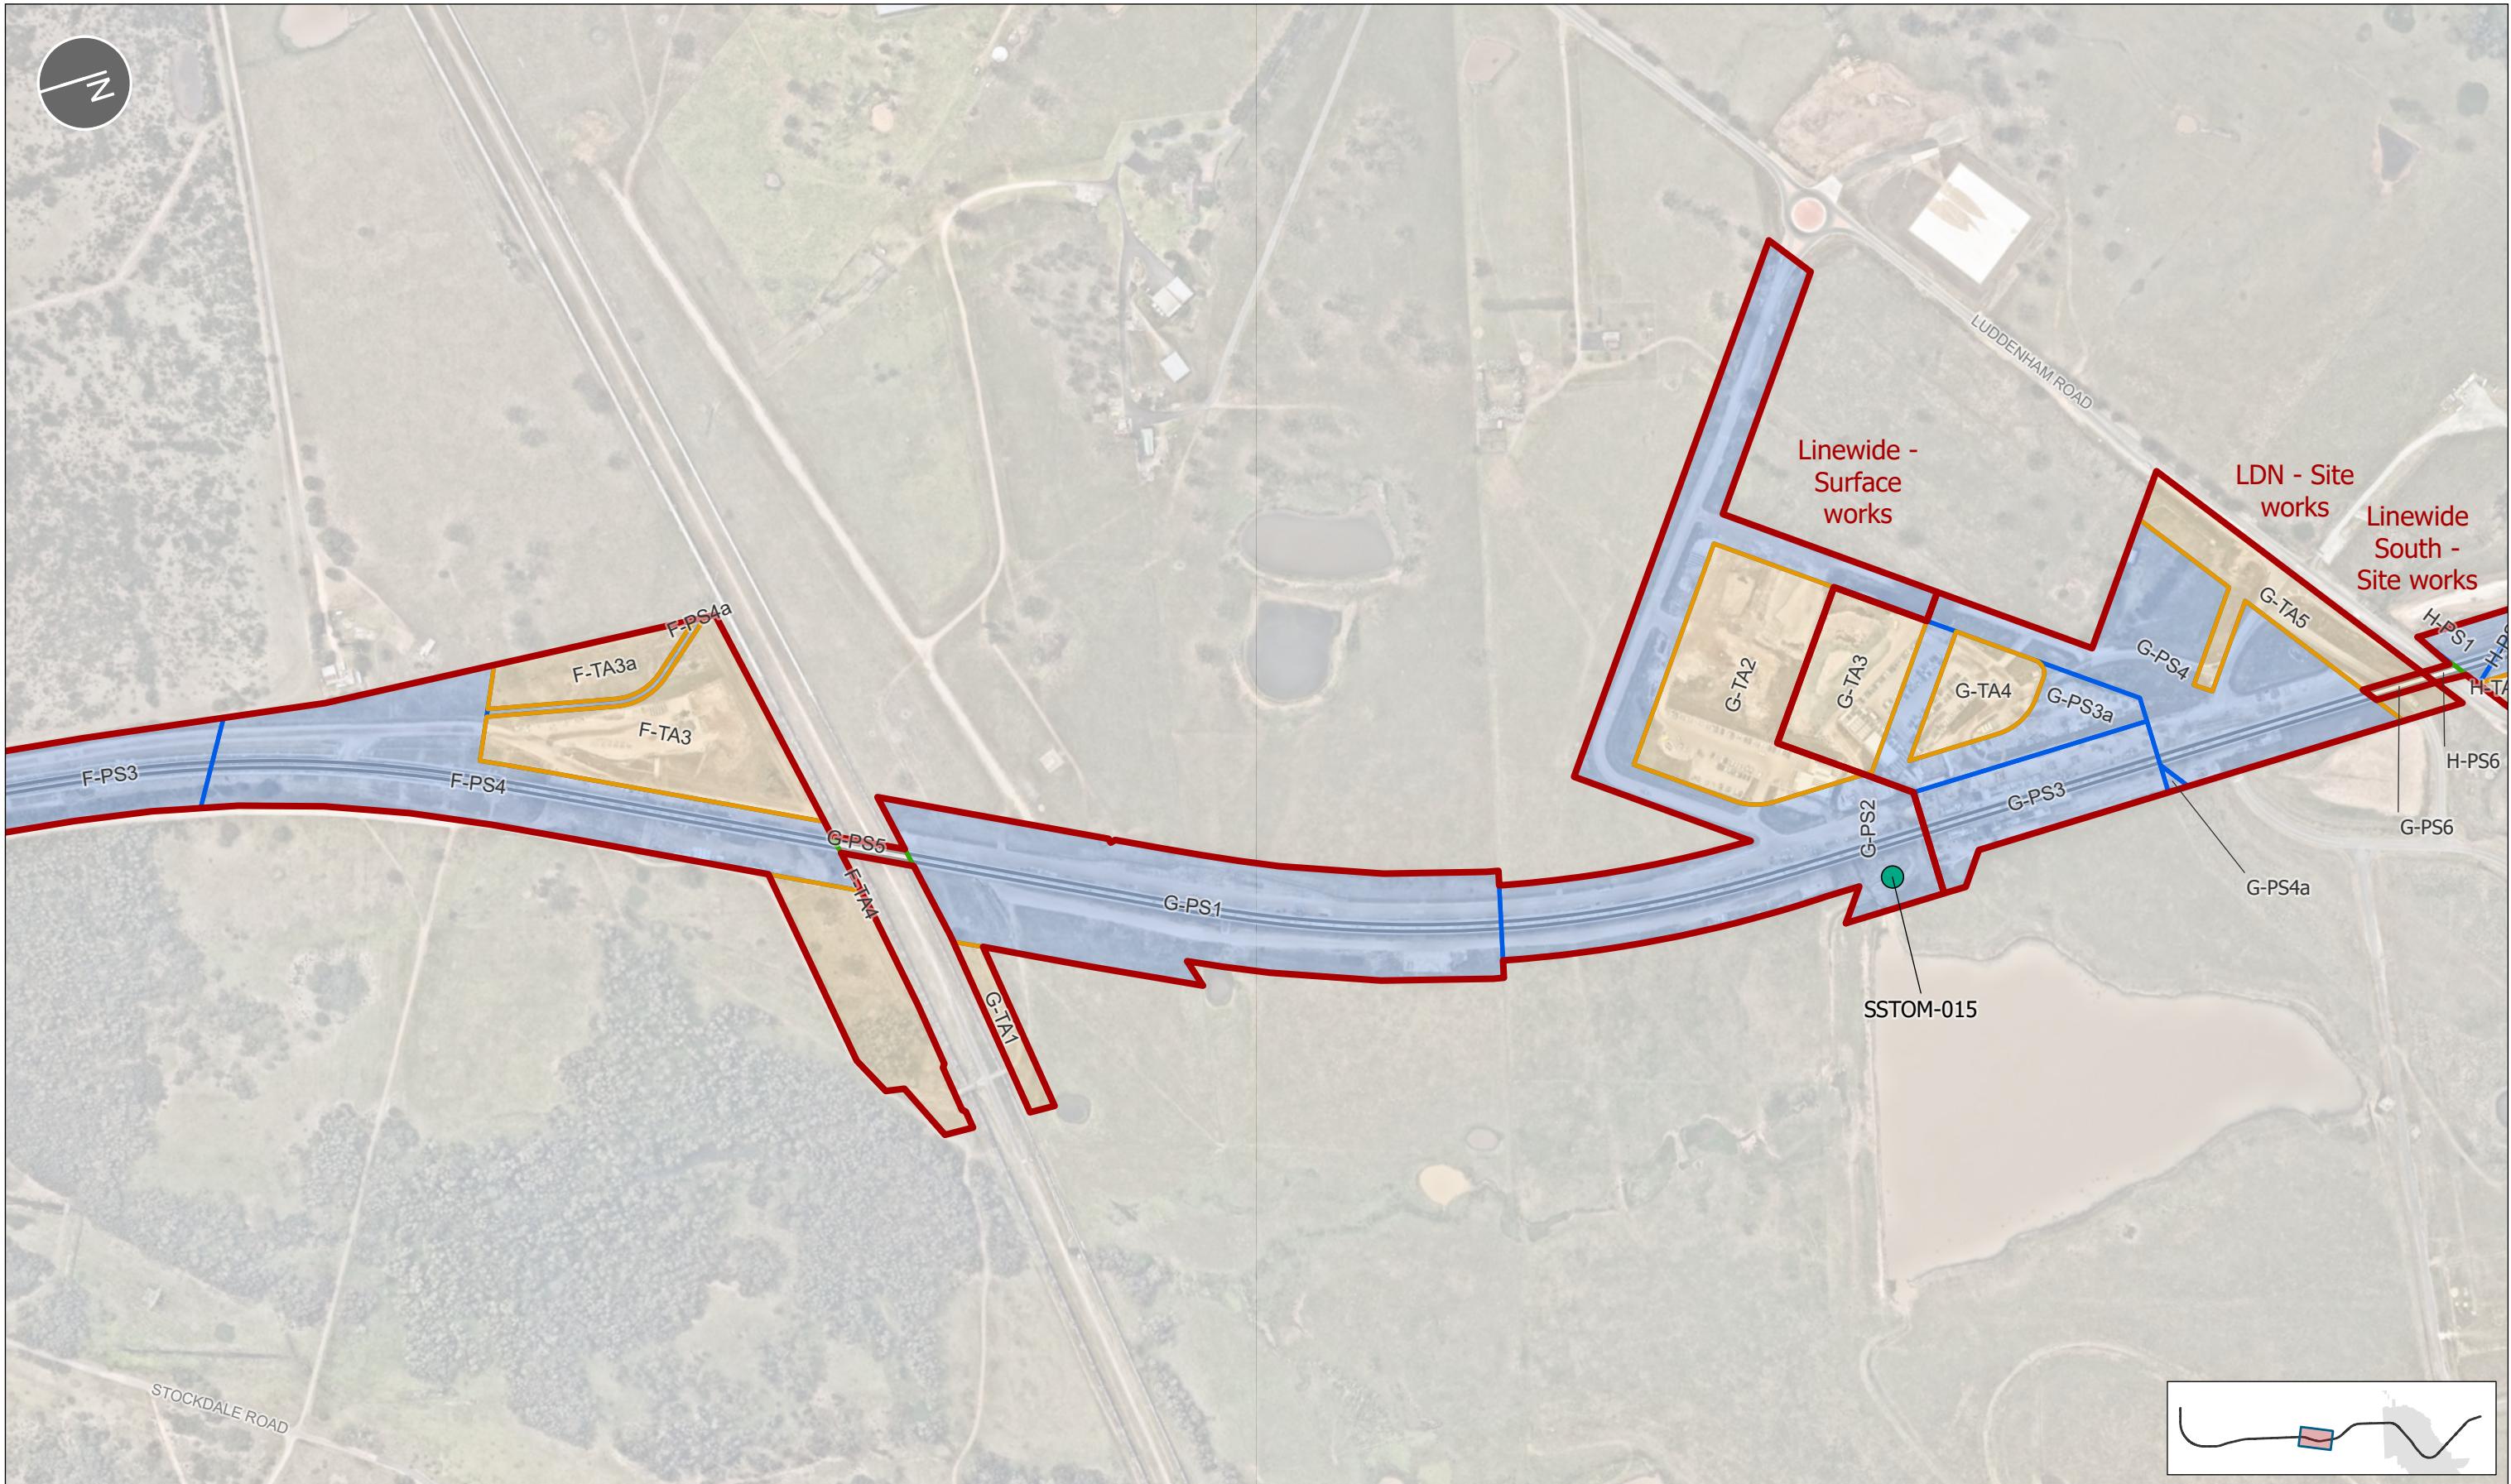


LEGEND	DISCHARGE POINTS	EPL PREMISE BOUNDARY	METRO ALIGNMENT	SITE ACCESS SCHEDULE	NOTES	REV	DATE	DESCRIPTION
Discharge Points	Temporary Sediment Basin	EPL Premise Boundary	Metro alignment	Aerial Stratum	EPL Premise Boundary Map	43	08.10.2025	Premise Map update
		Surface works	Watercourse	Project Site		44	28.10.2025	Premise Map update
		Sub-surface works	Western Sydney International boundary (WSP)	Temporary Area		45	04.11.2025	Premise Map update
						46	17.11.2025	Premise Map update
						47	05.12.2025	Premise Map update
						48	16.01.2026	Premise Map update



EPL 21807 PREMISE BOUNDARY


PROJECT Sydney Metro – Western Sydney Airport - SSTOM




SCALE 1:5,000  
0 100 200m

A3  
BY ROVED  
SHEET 7 of 12  
DATE 16/01/2026

MAP # SMWSASSM-PLD-1NL-ENV-GIS-000001\_48  
REV  
COORDINATE SYSTEM GDA2020 MGA Zone 56  
EW

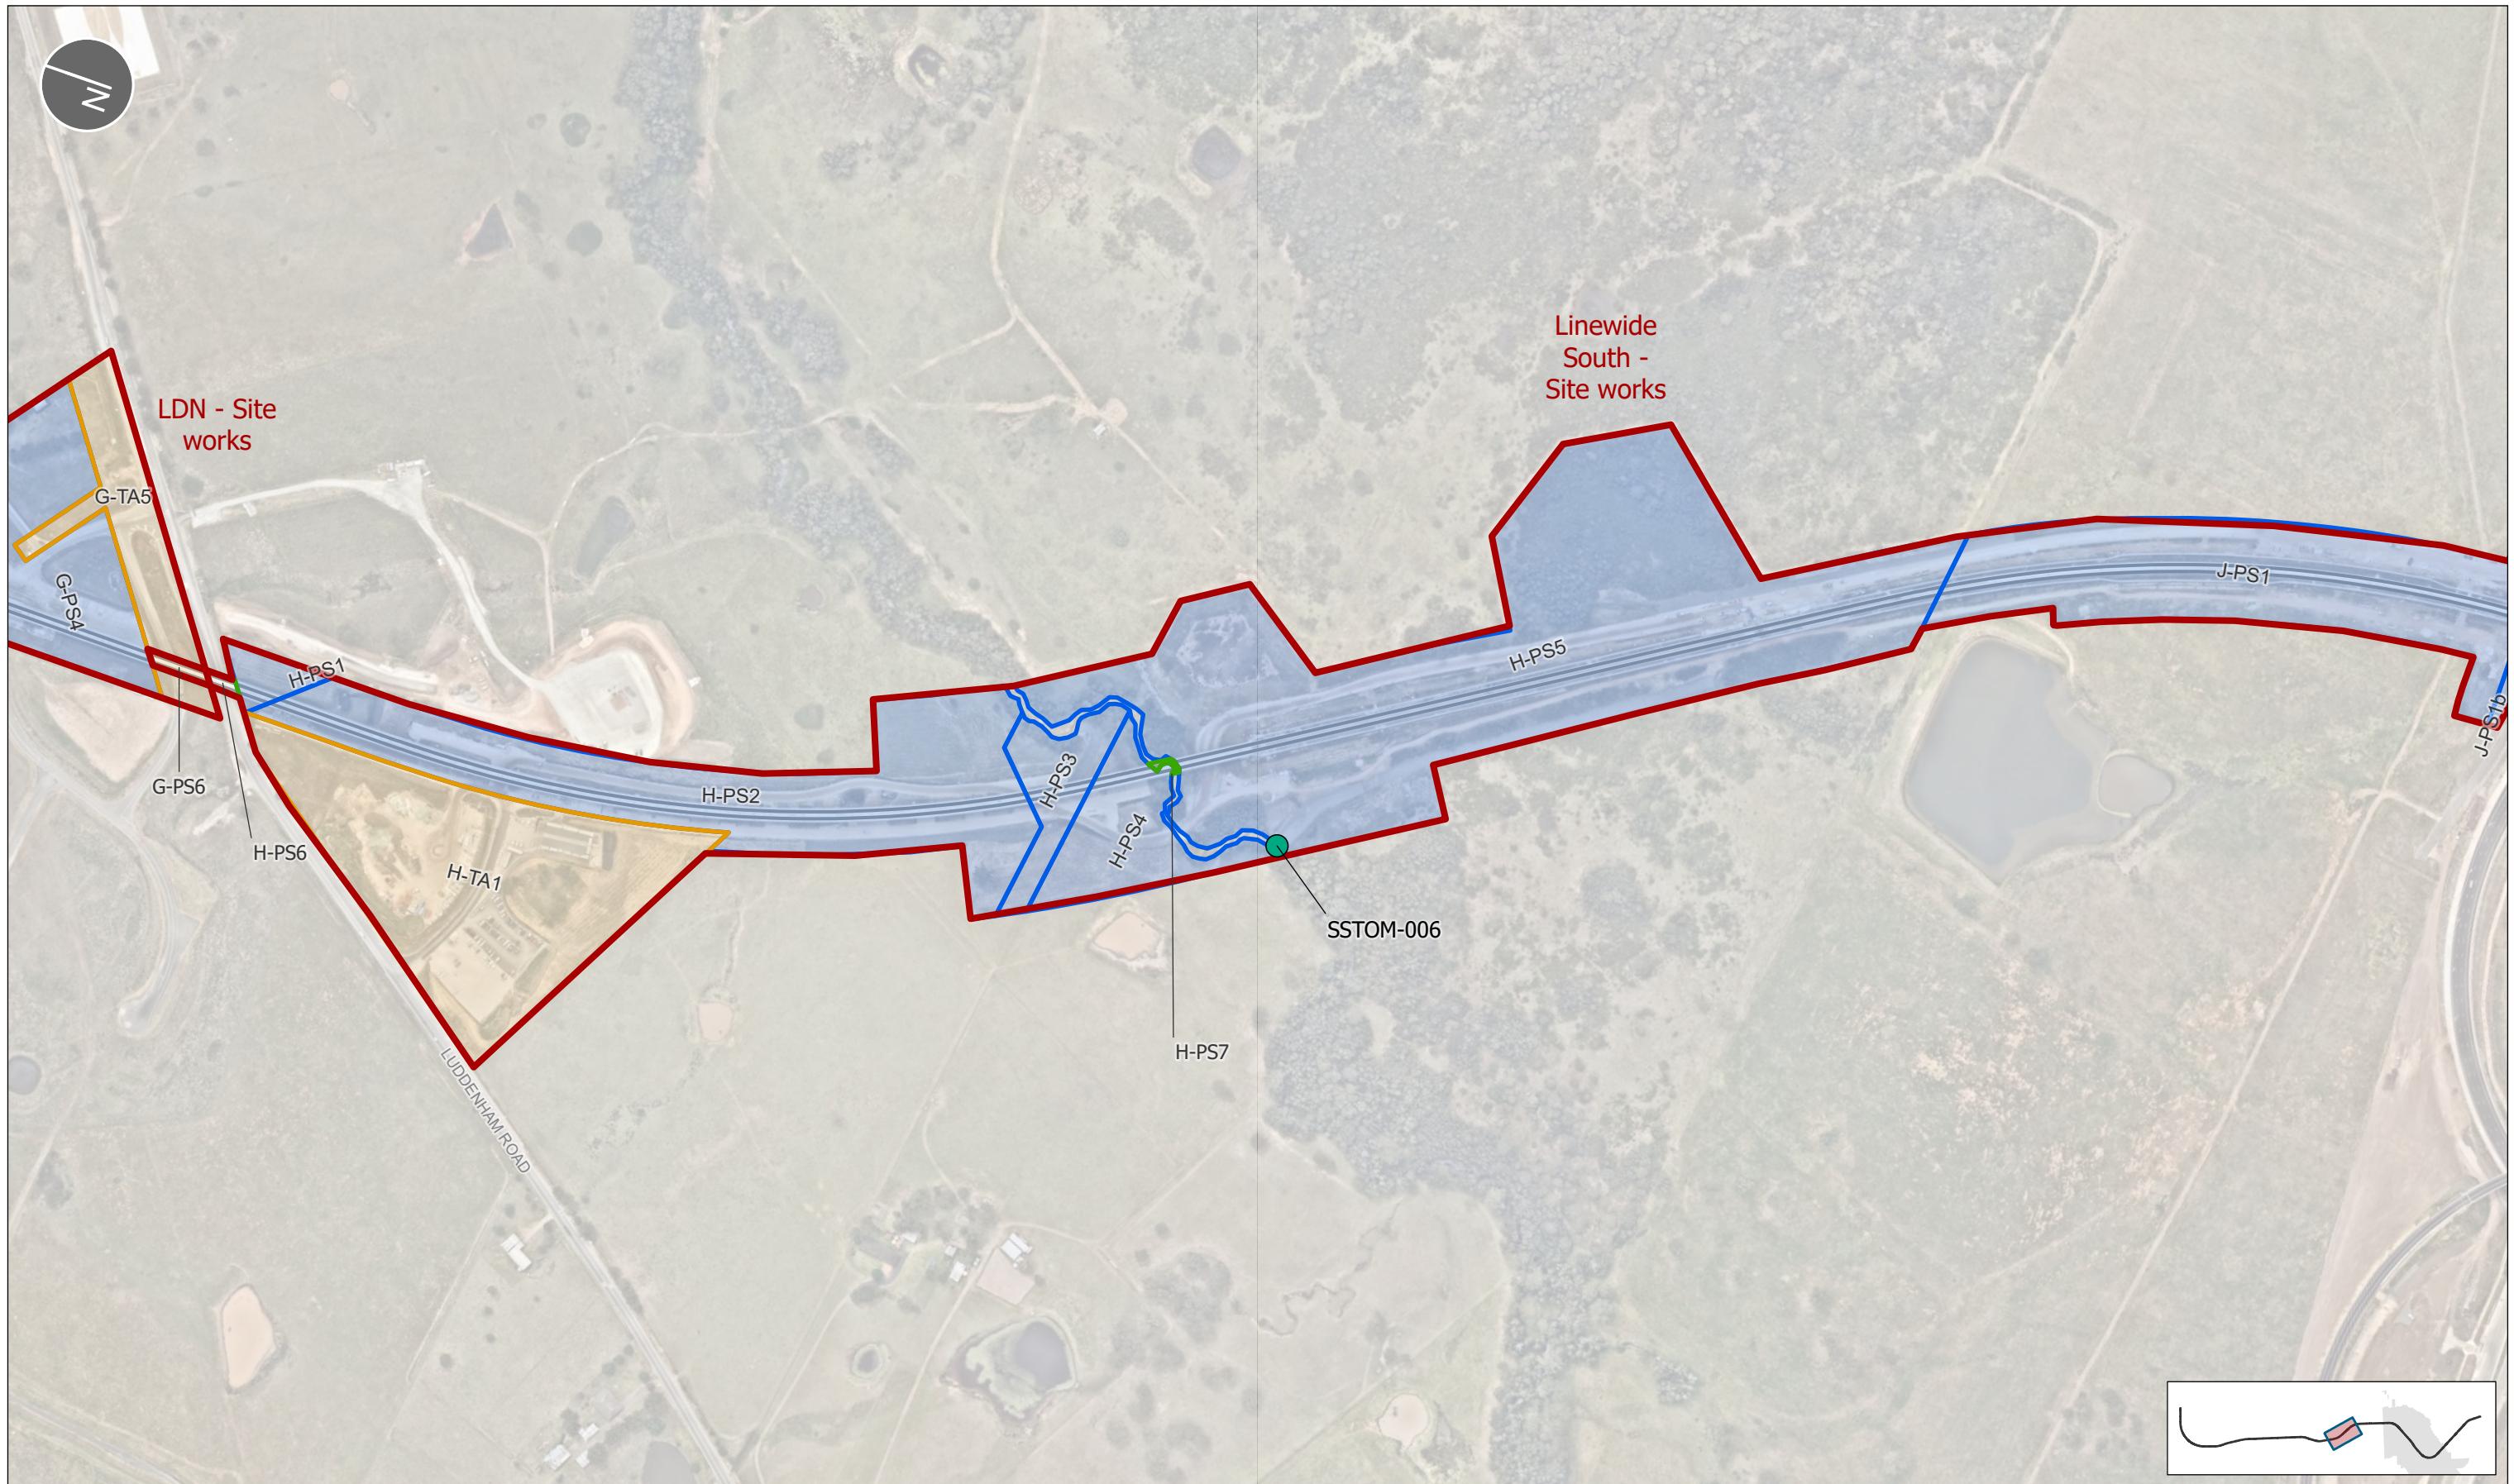


LEGEND		Site Access Schedule		NOTES		REV	DATE	DESCRIPTION
Discharge Points		Metro alignment		EPL Premise Boundary Map		43	08.10.2025	Premise Map update
Temporary Sediment Basin		Watercourse				44	28.10.2025	Premise Map update
	EPL Premise Boundary	Western Sydney International boundary (WSP)				45	04.11.2025	Premise Map update
	Surface works		Aerial Stratum			46	17.11.2025	Premise Map update
	Sub-surface works		Project Site			47	05.12.2025	Premise Map update
			Temporary Area			48	16.01.2026	Premise Map update
Discharge Points		Site Access Schedule		NOTES		EPL Premise Boundary Map		
Temporary Sediment Basin		Metro alignment						
	EPL Premise Boundary	Watercourse						
	Surface works	Western Sydney International boundary (WSP)						
	Sub-surface works		Aerial Stratum					
			Project Site					
			Temporary Area					
EPL Premise Boundary		PROJECT		CLIENT		Parklife Metro D&C		
Surface works		Sydney Metro – Western Sydney Airport - SSTOM		Sydney Metro				
Sub-surface works		TITLE		PROJECT				
		EPL 21807 PREMISE BOUNDARY		Sydney Metro – Western Sydney Airport - SSTOM				
		SHEET		CLIENT				
		8 of 12		Sydney Metro				
		SCALE		DATE				
		1:5,000		16/01/2026				
		0 100 200m		COORDINATE SYSTEM				
		GDA2020 MGA Zone 56		MAP #				
				SMWSASSM-PLD-1NL-ENV-GIS-000001_48				
REV 48								

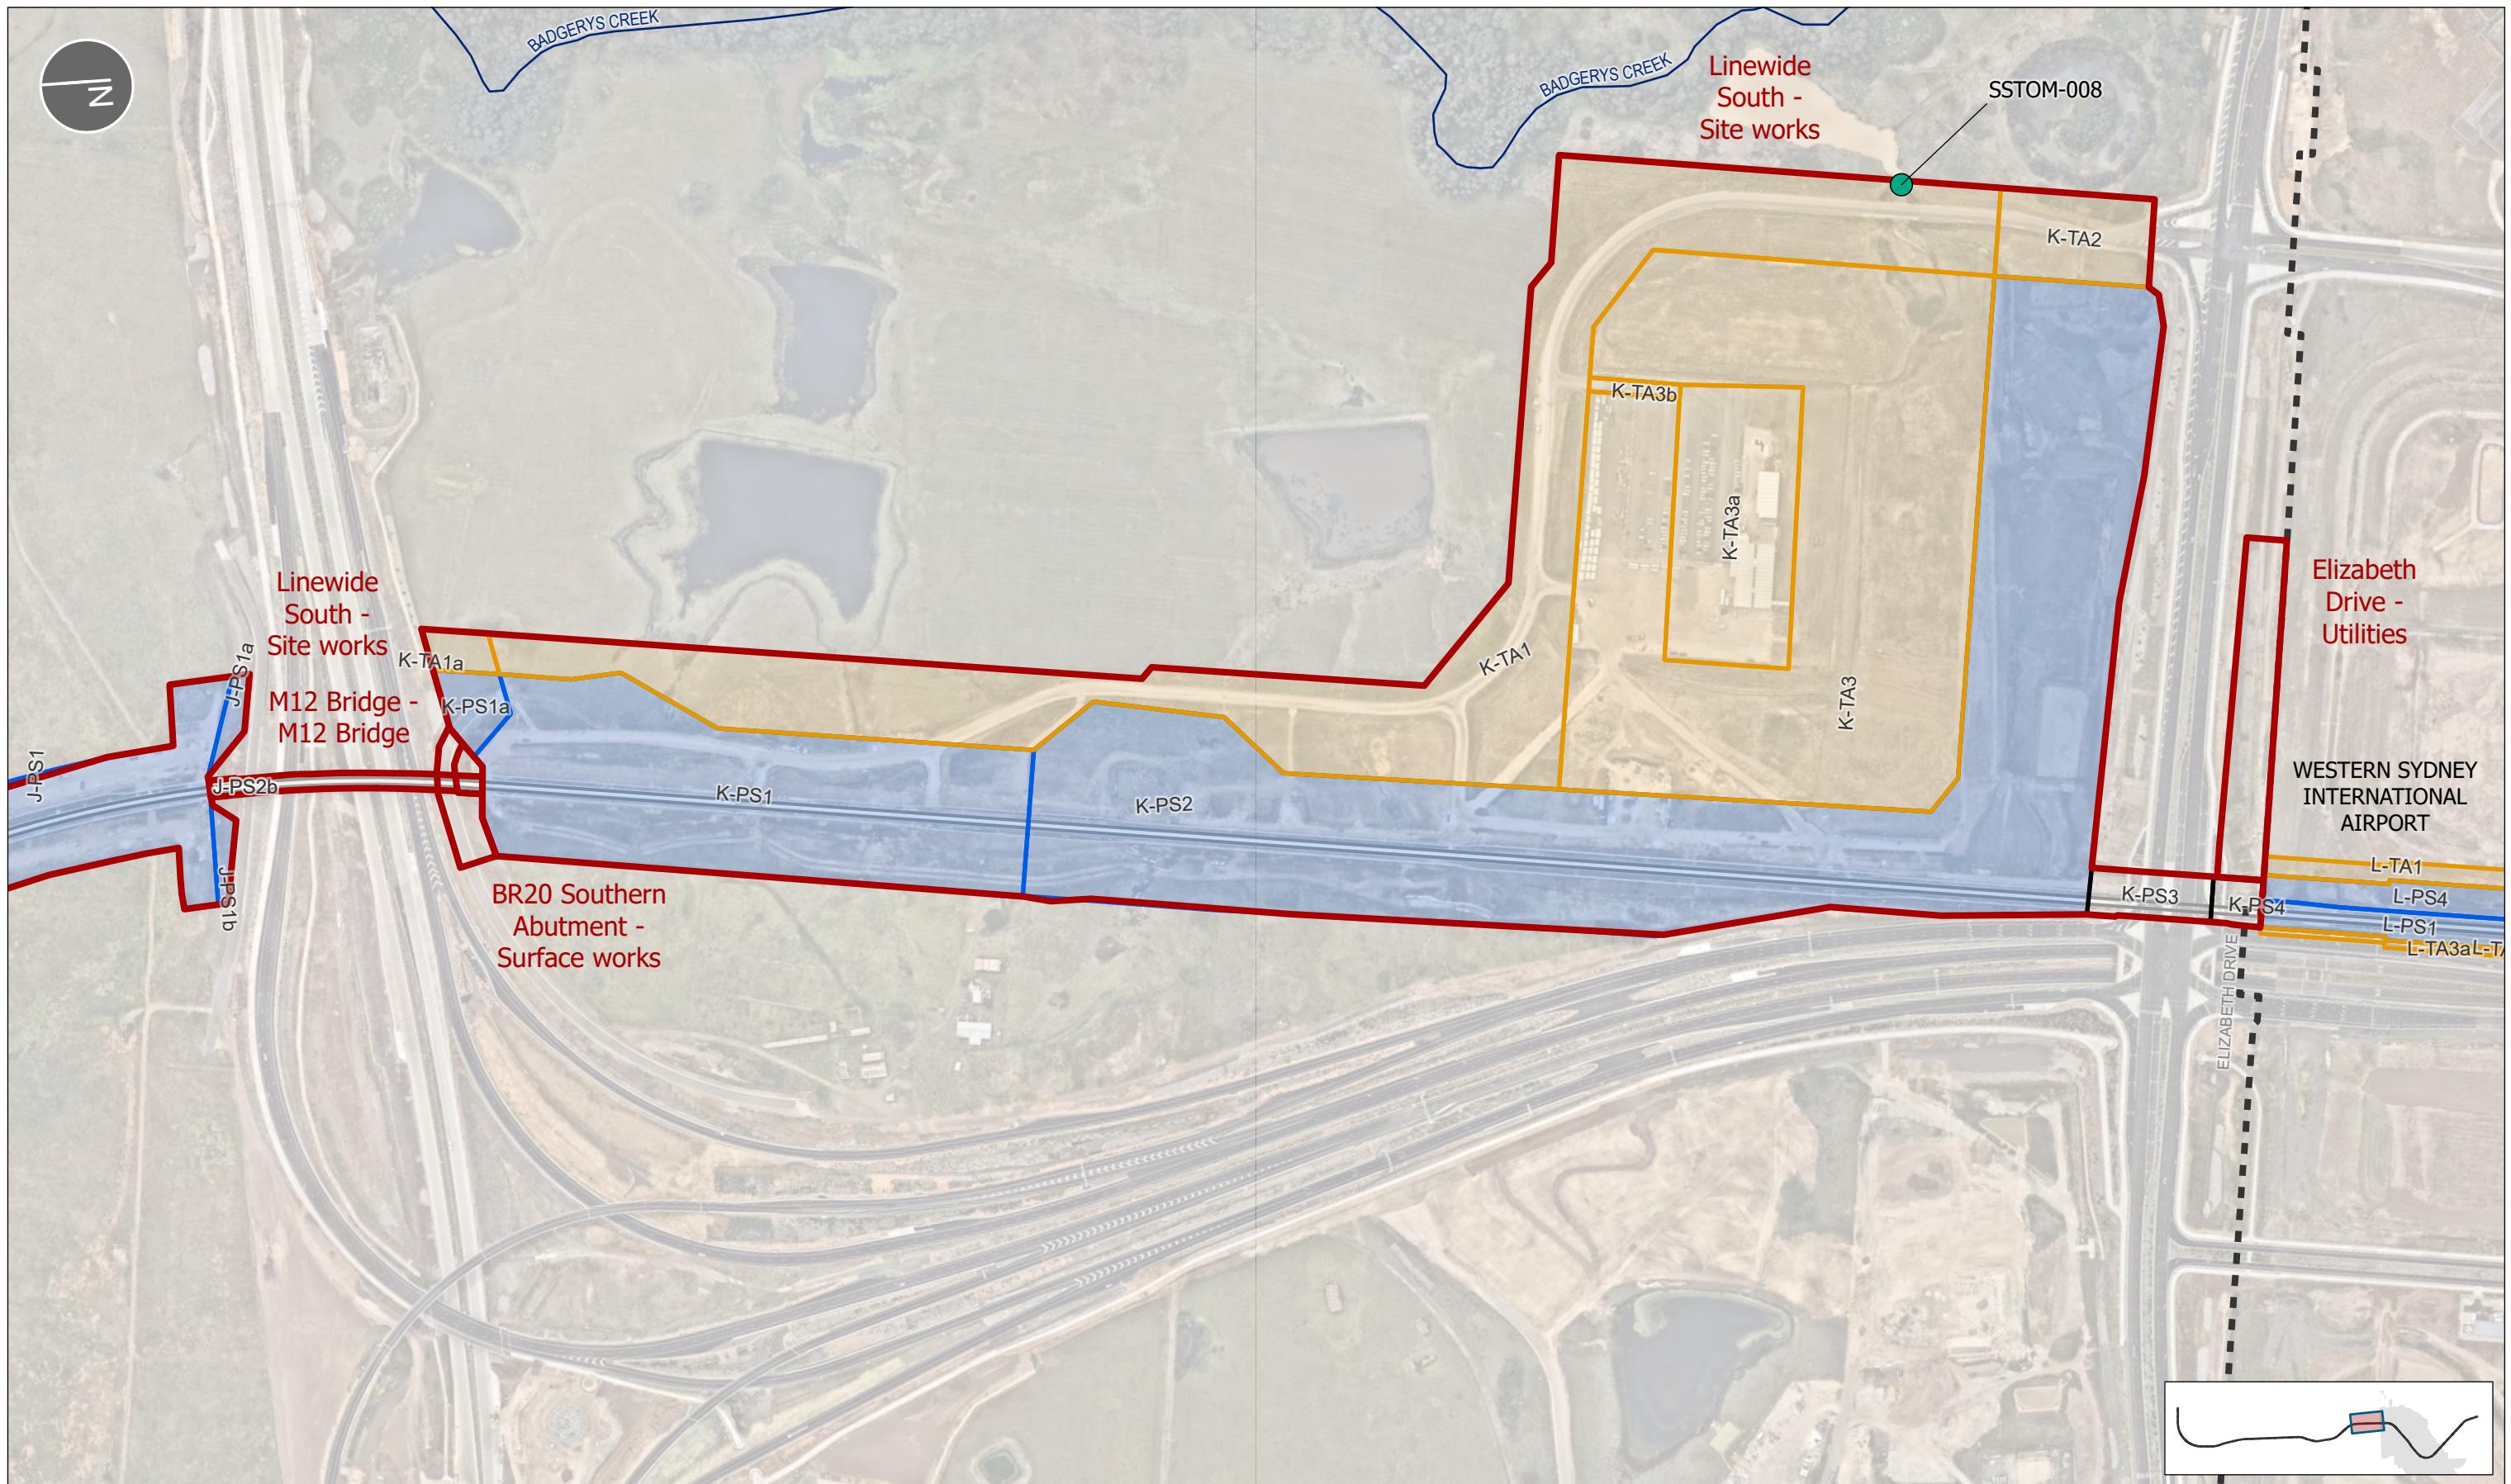

**LEGEND**

Discharge Points      EPL Premise Boundary      Metro alignment  
 Temporary Sediment Basin      Surface works      Watercourse  
 Sub-surface works      Western Sydney International boundary (WSP)      Aerial Stratum  
 Project Site      Substratum

Temporary Area

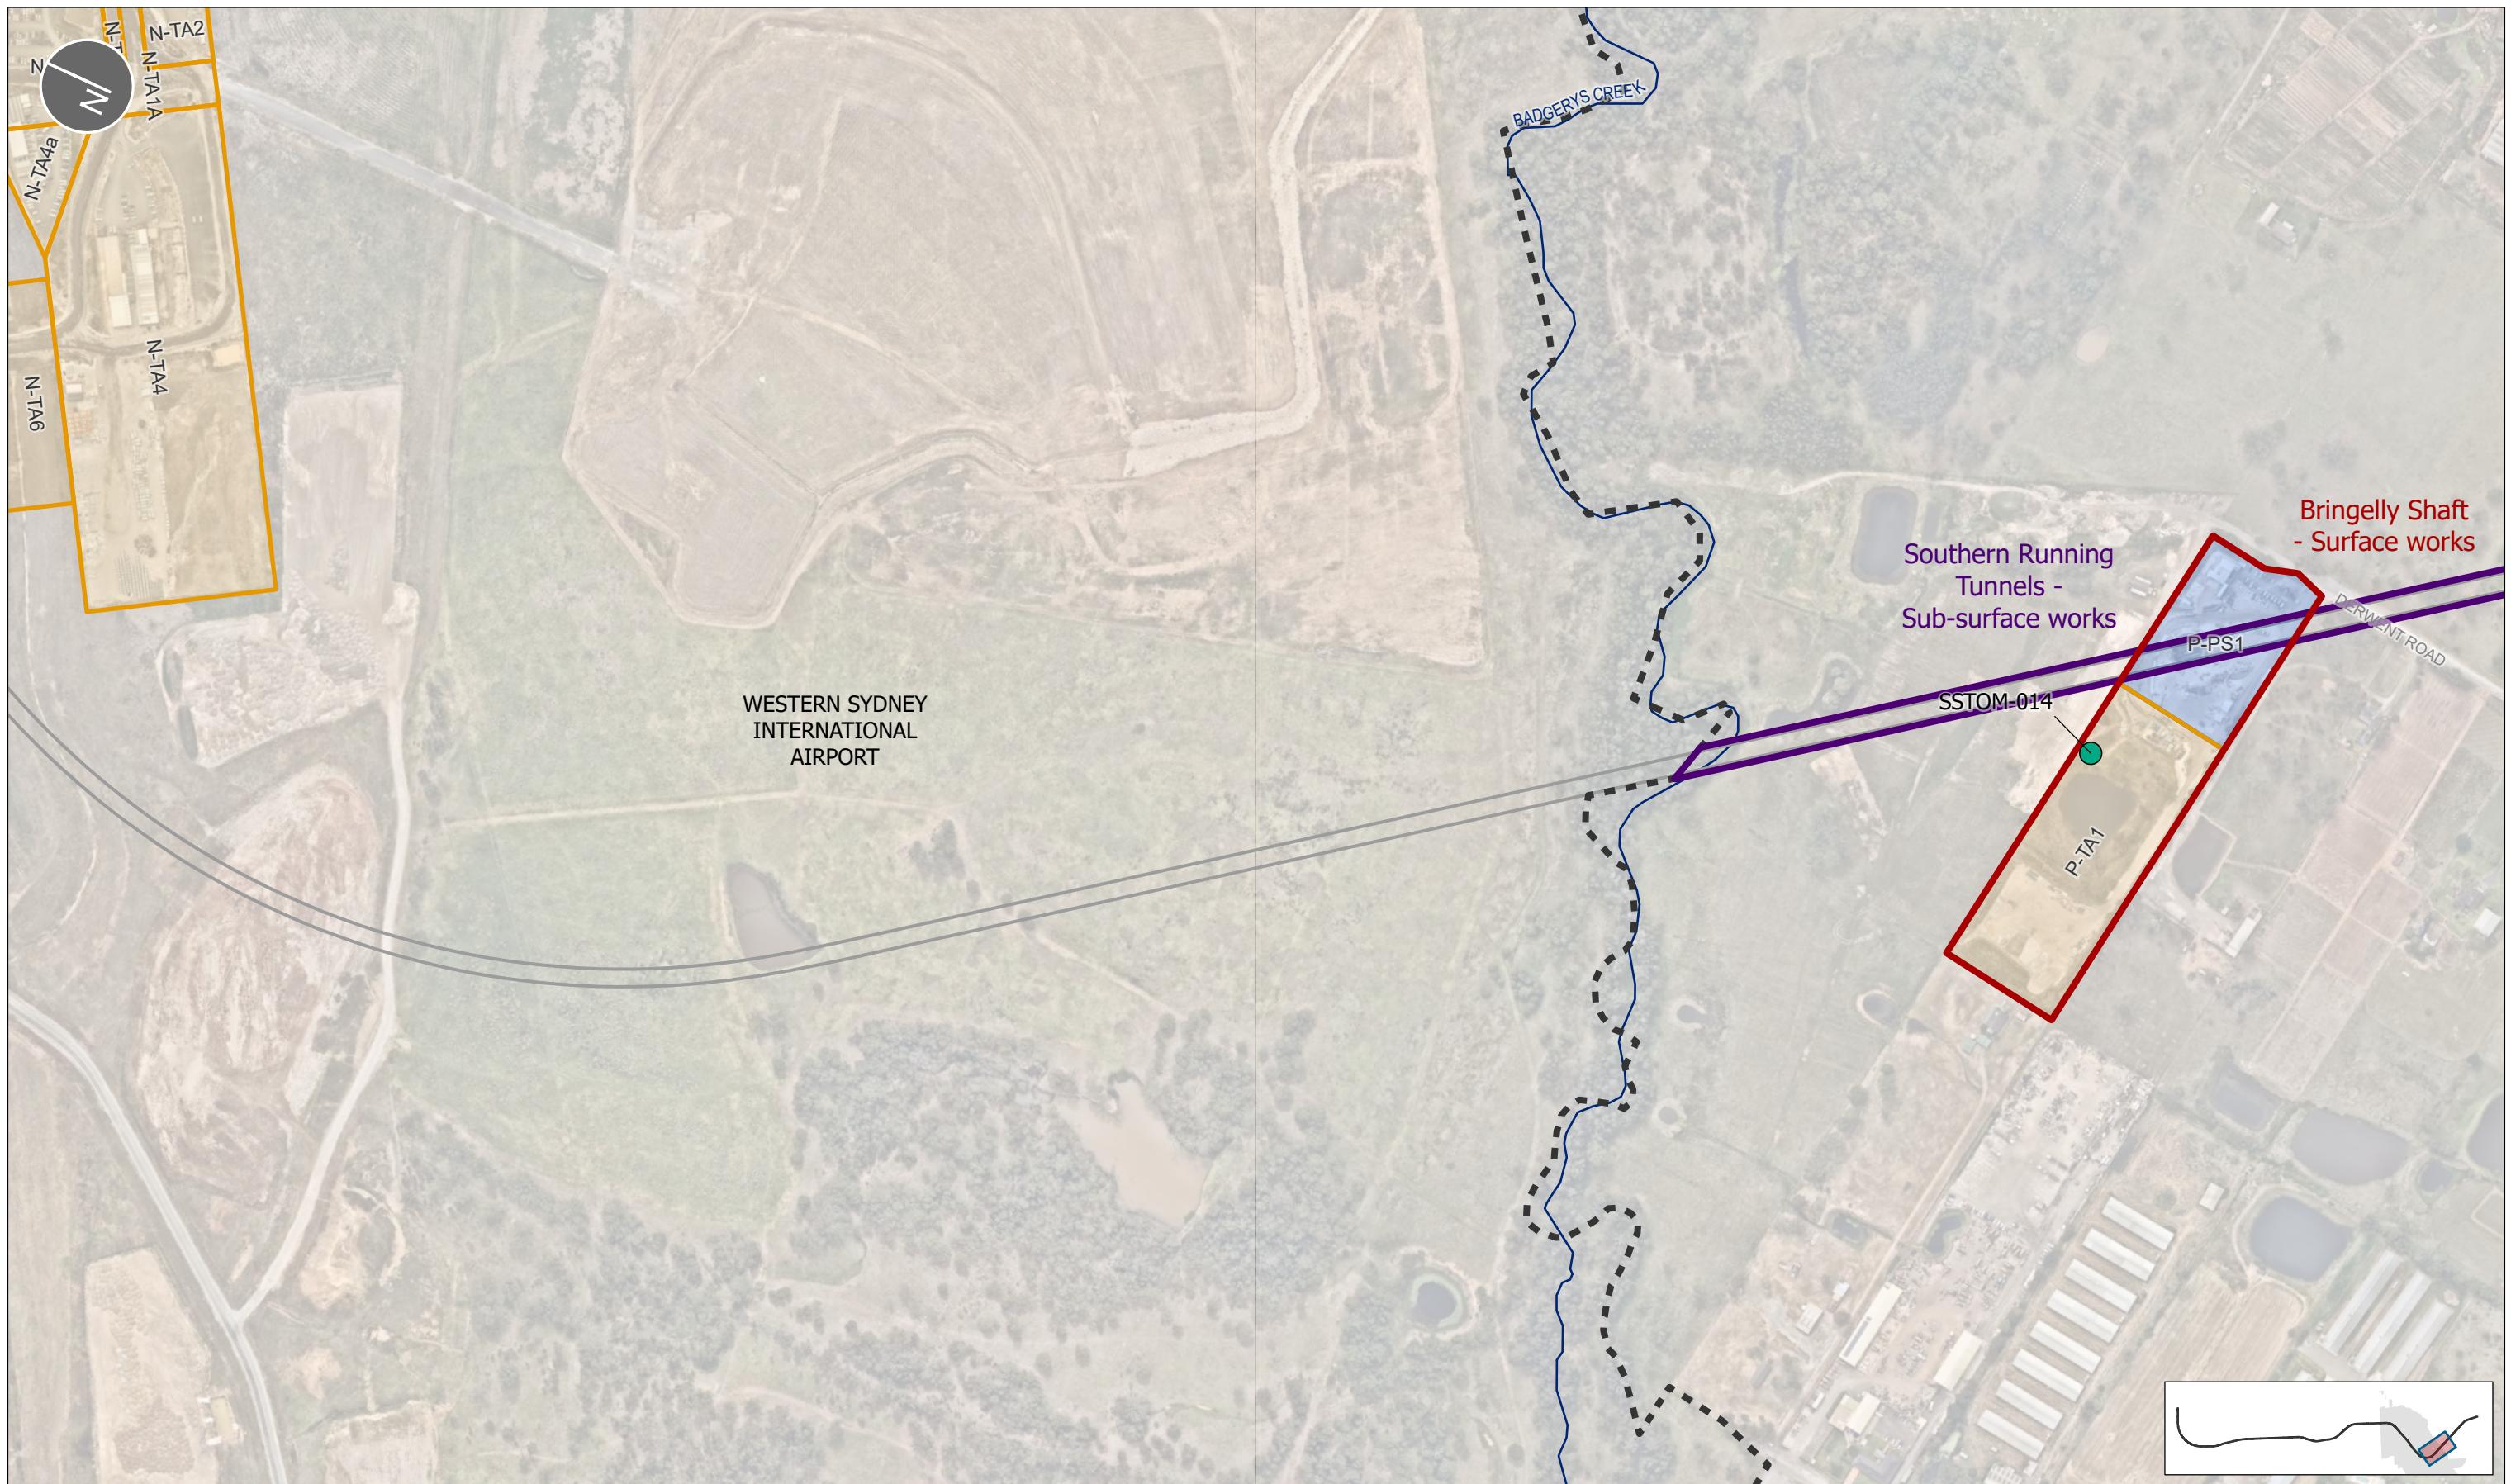

LEGEND

Discharge Points      EPL Premise Boundary      Metro alignment

Temporary Sediment Basin      Surface works      Watercourse

Sub-surface works      Site Access Schedule      Project Site

Western Sydney International boundary (WSP)      Temporary Area

**NOTES**

EPL Premise Boundary Map

REV DATE DESCRIPTION

43 08.10.2025 Premise Map update

44 28.10.2025 Premise Map update

45 04.11.2025 Premise Map update

46 17.11.2025 Premise Map update

47 05.12.2025 Premise Map update

48 16.01.2026 Premise Map update

**TITLE**  
EPL 21807 PREMISE BOUNDARY

**PROJECT**  
Sydney Metro – Western Sydney Airport - SSTOM

**CLIENT**  
Sydney Metro

**SCALE**  
1:5,000

**MAP #**  
SMWSASSM-PLD-1NL-ENV-GIS-000001\_48

**REV**  
48


**A3**      BY **ROVED**

**0**      100      200m


**SHEET**  
10 of 12

**COORDINATE SYSTEM**  
GDA2020 MGA Zone 56

**DATE**  
16/01/2026

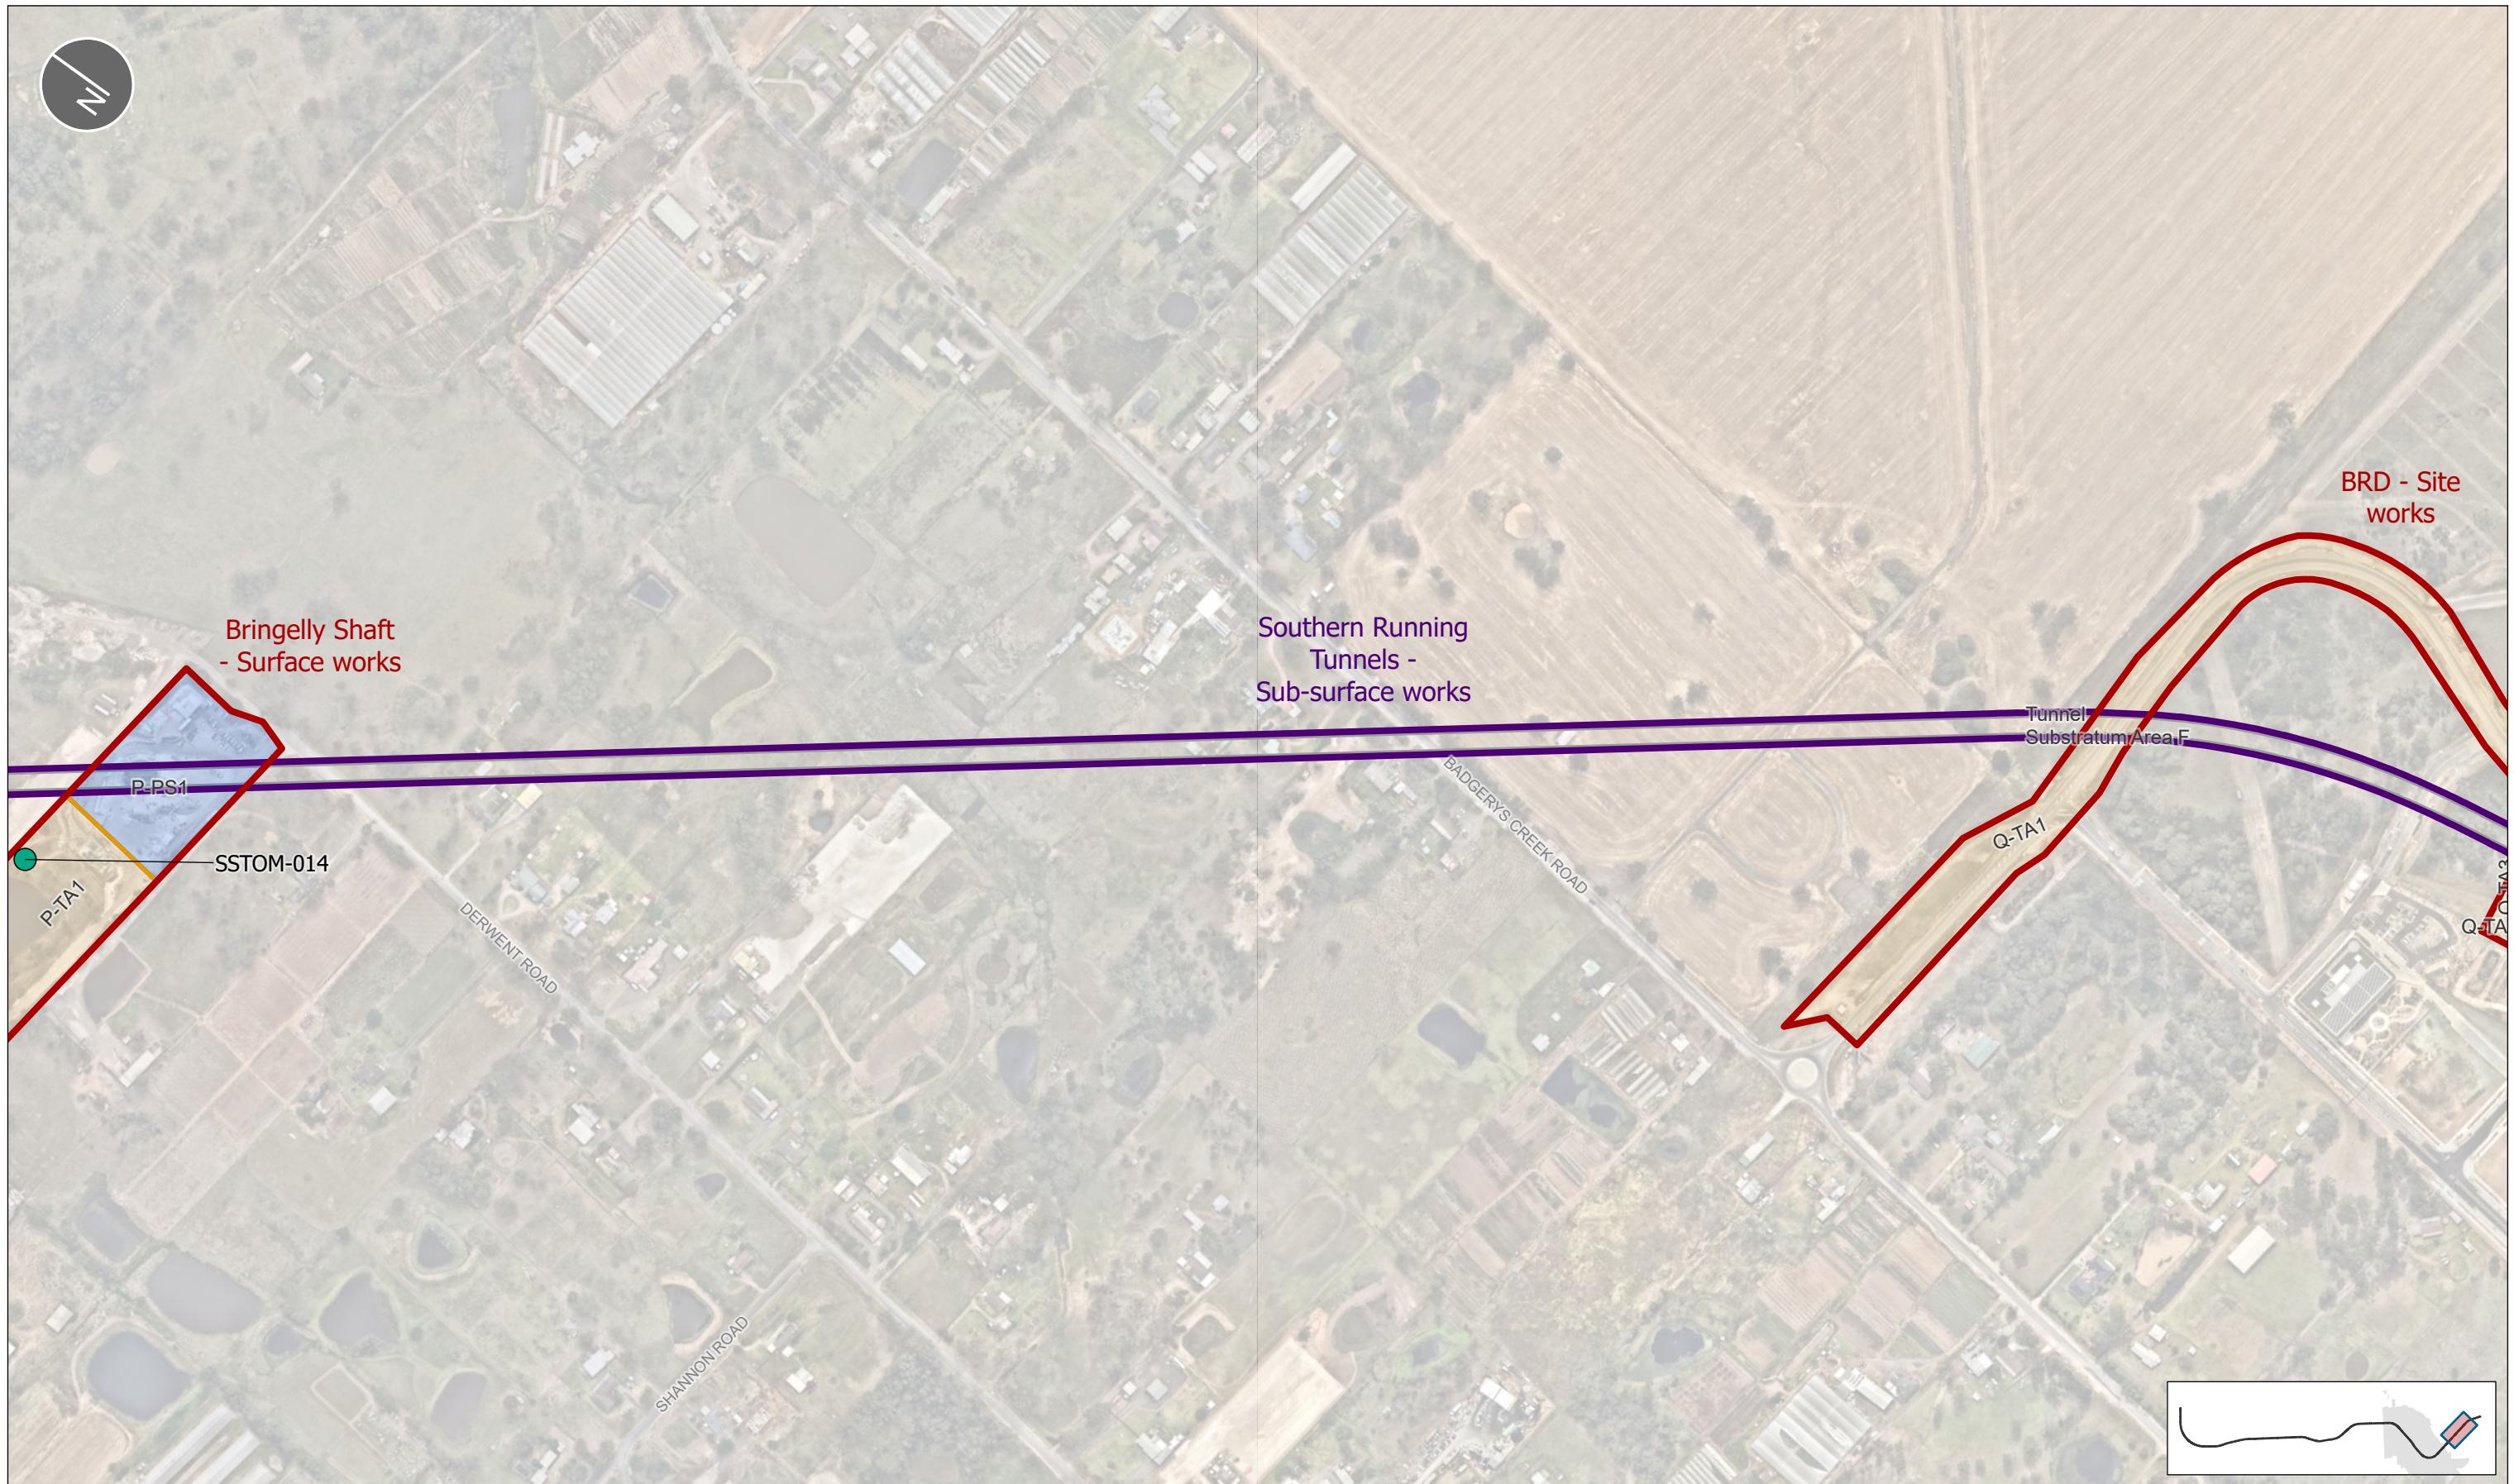

LEGEND		NOTES		REV	DATE	DESCRIPTION
Discharge Points	EPL Premise Boundary	Metro alignment	Site Access Schedule	43	08.10.2025	Premise Map update
Temporary Sediment Basin	Surface works	Watercourse	Project Site	44	28.10.2025	Premise Map update
	Sub-surface works	Western Sydney International boundary (WSP)	Substratum	45	04.11.2025	Premise Map update
			Temporary Area	46	17.11.2025	Premise Map update
				47	05.12.2025	Premise Map update
				48	16.01.2026	Premise Map update
		EPL Premise Boundary Map				
		TITLE EPL 21807 PREMISE BOUNDARY		PROJECT	Sydney Metro – Western Sydney Airport - SSTOM	
		CLIENT		Sydney Metro		
		SCALE	1:5,000	A3	WIN BY	ROVED
		COORDINATE SYSTEM	GDA2020 MGA Zone 56	11 of 12	IEW	MAP #
		DATE	16/01/2026			SMWSASSM-PLD-1NL-ENV-GIS-000001_48

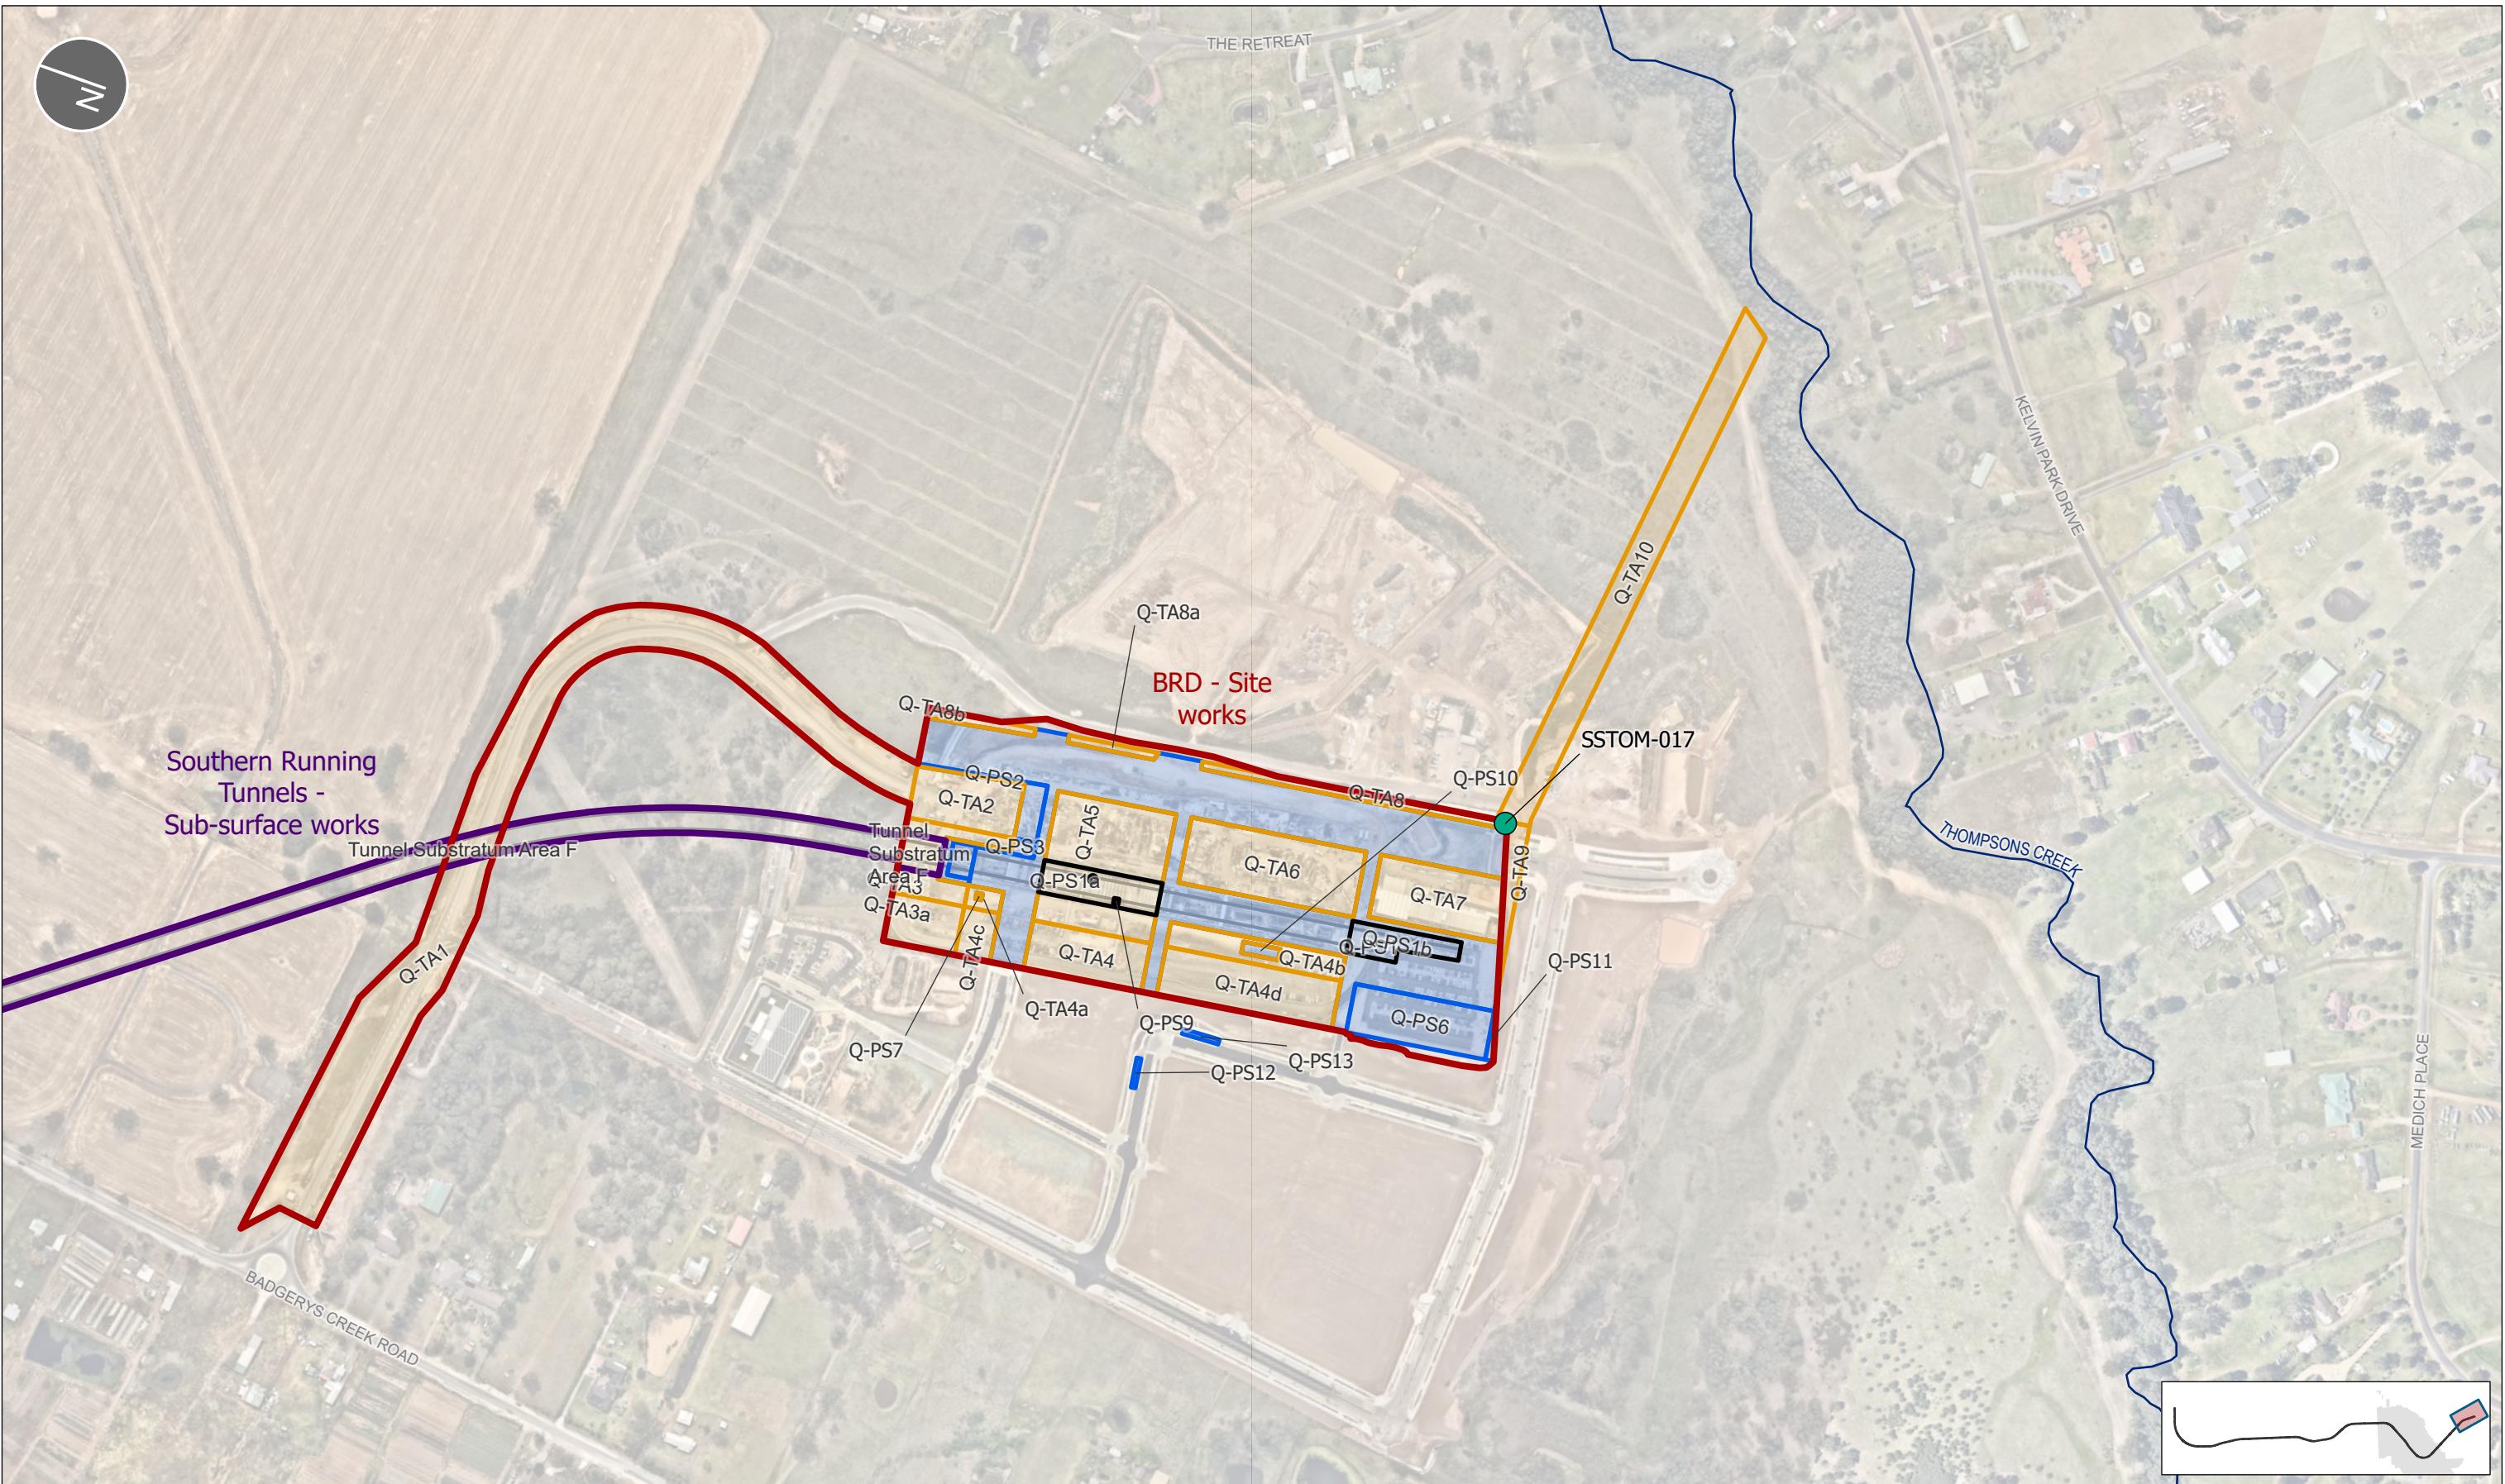

LEGEND	
Discharge Points	EPL Premise Boundary
Temporary Sediment Basin	Metro alignment
Water Treatment Plant	Surface works
	Sub-surface works

■	Project Site
■	Substratum
■	Temporary Area
■	Watercourse

■	Western Sydney International boundary (WSP)
■	Metro alignment

■	Site Access Schedule
■	Project Site
■	Substratum
■	Temporary Area



NOTES  
EPL Premise Boundary Map

REV	DATE	DESCRIPTION
43	08.10.2025	Premise Map update
44	28.10.2025	Premise Map update
45	04.11.2025	Premise Map update
46	17.11.2025	Premise Map update
47	05.12.2025	Premise Map update
48	16.01.2026	Premise Map update

TITLE  
EPL 21807 PREMISE BOUNDARY

SCALE  
1:5,000

0 100 200m

PROJECT  
Sydney Metro – Western Sydney Airport - SSTOM

CLIENT  
Sydney Metro

MAP #  
SMWSASSM-PLD-1NL-ENV-GIS-000001\_48

BY  
A3  
ROVED

DATE  
16/01/2026
